(This SWPPP Template is for the Common Plan Permit Only, and does NOT address SWPPP requirements found in the CGP.)

Common Plan SWPPP for

Megroz Residents 3605 East Middle Fork Road

Eden Ut, 84310

Chris Megroz

Solitude Builders LLC

2068 E 5950 N Liberty Ut,84310

Date
August 16,2017



1. Project Information

Common Plan Permit Project Name: Megroz Residents Address: 3605 East Middle Fork Road City: Eden State: UT Zip: 84310 Latitude: 41 19' 25.25 N Longitude: 111 48' 25.91" W UPDES Permit Tracking Number: UTRH82183 Owner: Chris Megroz Contact Person: Carson Young Address: 3605 E Middle Fork Road City:Eden State Ut Zip:84310 Telephone Number: 801 452 5020 Email Address: chrismegroz@gmail.com General Contractor: Solitude Builders LLC Contact Person: Carson Young Address: 2068 E 5950 N City:Liberty State:UT Zip:84310 Phone: 801 452 5020 Email Address: cwy185@hotmail.com 2. Pollution Sources/Best Management Practices

Answer yes or no whether the following features are located at your site. If yes, select the BMP(s) that will be used to protect each feature. If no, continue to the next question. Attach necessary illustrated details for proper installation in Appendix L, and show locations of all controls on Site Map in Appendix B.

Is there a SWPPP sign on site? (see permit part 1.10) No □ Yes x The sign must include the UPDES tracking number, the owner or general contractor name, phone number and email, and if the SWPPP is on-line, instructions on how to view it. 2.2 Will there be non-stormwater discharges on the site? (see permit part 1.3) Yes □ No x Construction Dewatering (if discharged offsite) must be covered by UPDES Permit UTG070000 (see permit part 2.7). Further, cleaning of tools and equipment must be contained in a plastic lined pit (see permit part 2.4.5 & 2.9).

2.3		lands, sensitive areas, or UK e permit part 2.2)	C wells located on or adjace	nt to the	Yes □	No x
	BMP(s)	□ Vegetative Buffers	□ Berms	□ Wattles		
		☐ Boundary Fence	□ Silt Fence			
	□ Other: Click here to enter text.					
2.4	Will the	e will conta	Yes □	No x from		
	the stockpiles CANNOT be placed in the street. (see permit part 2.1.1)					
	BMP(s)	x Silt Fence	x Staked Straw Wattle	x Covering		
	□ Other: Click here to enter text.					
	☐ Contained by other BMP. Explain: Click here to enter text.					

2.5	Are surf disturba Is there	h	Yes □	No x						
	used, yo	30' natural vegetative buffer u must demonstrate that the vegetative buffer, and select	additional con	trols offer the	e same prote	ection as a	<i>30</i> ′			
	BMP(s):	x 30' Natural Vegetative But	x Less than 1 acre Disturbance							
		x 2 Silt Fence Barrier		□ 2 Straw Wa	ttle Barrier:	s (Fiber Ro	oll)			
		☐ Less than 30' Natural Veg text.	etative Buffer.	Additional Cor	ntrols: Click	here to e	enter			
2.6	Does you 2.3.2)	ur site have steep slopes (gr	eater than 70%	6)? (see permit	part	Yes □	No x			
	BMP(s):	☐ Erosion Control Blanket	□ Minimum Di	sturbance	□ Seeding					
		□ Hydroseed	□ Mulch		□ Takifiers					
		□ Other: Click here to ent	er text.							
2.7	What pe	rimeter and sediment contr	ols will be used	d on the site?	(see permit p	part 2.1.2 8	t 2.3)			
	BMP(s):	x Silt Fence	□ Straw Wattl Rolls)	es (Fiber	□ Sediment Trap					
		□ Sediment Basin	x Swales		x Berms					
		x Vegetative Buffer	□ Cut-Back-Cu	urb						
		☐ Other: Click here to enter	r text.							
2.8	What storm drain inlet protection will be used on this site? (see permit part 2.1.3)									
	Where is/are the nearest downstream inlet(s): Click here to enter text.									
	BMP(s):	☐ Rock/Sand-filled Bags	□ Drop Inlet B	ags	□ Inlet Wa	ttles				
		□ Filter Fabric								
		□ Other: Click here to enter	r text.							
2.9	Will curb	ramps be used at the site?				Yes □	No x			
		curb ramps are used it must ter. (see permit part 2.4.2)	be done with m	naterial that w	vill not wash	away in				
	BMP(s):	□ Crushed Rock	□ Wood Dunna	age						
		□ Other: Click here to ent								

2.10	What du	ust control BMP(s) will be use	control BMP(s) will be used?							
	BMP(s):	x Wetting with Water								
		□ Other: Click here to ent	er text.							
2 11	\\/h = 4 4 4 4	ack out control will be used on the site? (see permit part 2.4.1)								
2.11			on the site? (see permit part 2	2.4.1)						
	BMP(s):	x Track Out Pad	□ Cobble	x Gravel						
		☐ Rumble Strips	☐ Wash Down Pad	□ Delivery Pad						
		☐ Limited Site Access	☐ Selective Access During D	ry Weather						
		□ Other: Click here to ent	er text.							
2.12	How will	l solid waste be dealt with o	n the site? (see permit part 2.	4.3)						
	BMP(s):	□ Bag Lightweight Trash	x Leak Proof Dumpsters	☐ Receptacles with Lids						
		□ Other: Click here to ent	er text.							
2.13	How will	non-aqueous liquid waste (oil solvent fuel) he dealt v	vith on the site?						
	DM((3).	☐ Contained and Removed from the site. ☐ Collected for Reuse ☐ Other: Click here to enter text.								
2.14	How will	spoils (extra or left over di	rt) be contained/managed?							
	BMP(s):	□ Cover Erodible Material	☐ Runoff Containment	x Haul Off Policy						
		□ Other: Click here to ent	er text.							
2.15		sanitary waste be handled								
	BMP(s):	x Portable Toilet(s) (must be	staked down & 10' from cur	b)						
		☐ Onsite or Adjacent Indoor	Bathrooms							
		□ Portable Toilet Secondary	Containment							
		□ Other: Click here to enter	er text.							
2.16	How will	concrete wash water be co	ntained on the site? (see per	mit part 2.4.5 & 2.9.1)						
	BMP(s):	x Lined Depression	□ Steel Dump	oster						
		☐ Regional Washout (per dev	velopment)							
		□ Other: Click here to ente	er text.							

SAUCONNOCHWITTEN	en year and a state of the stat		POTATO SELECTION TO THE PARTY OF THE PARTY O						
2.17	What co	ontrols will be used for const	ruction materials store	ed on site?					
	BMP(s):	x Covering Erodible or Liqui	ndary Containment						
		☐ Strategic Storage and Sta	ging						
		□ Other: Click here to ent	er text.						
2.18	What co	at controls will be in place for equipment fueling, maintenance, and washing?							
	BMP(s):	□ Fueling w/Mobile Track w	/Spill Kit 🗆 Offsit	e O+M					
		Other: No equipment fueling	ng or maintenance , was	hing will take place on site.					
2.19	How wil	How will sediment be contained on site until home owner completes landscaping?							
	BMP(s):	☐ Landscaping	□ Swales	□ Rock Filters					
		x Perimeter Controls	x Vegetated Buffer	x Native Vegetative Barriers					
		□ Cut-Back-Curb	☐ Leave Front-Yard Lo	wer than Sidewalk					
		□ Other: Click here to ent	er text.						
		aintenance required to ensur re of compromised BMP.	e proper BMP functionir	ng must be done within 72 hours					
3. S	ite Ma	ap *							
dimen	sions), pl			rings that show site layout and ndix B) showing the layout of					
	boundaries of project/property								

- 2. boundaries of disturbance (including areas outside of property boundaries)
- 3. show slopes on site
- 4. location of structures/facilities
- 5. locations of:
 - a. stockpiles for soils and materials
 - b. construction supplies
 - c. portable toilets
 - d. garbage/trash containers
 - e. egress points/track out pads

- f. concrete washout pits or containers
- 6. water bodies, wetlands, natural vegetative buffers
- 7. placement of all BMPs, perimeter, erosion control, sediment control, inlet, etc.
- 8. storm water inlets and storm water discharge points (where storm water drains off the site)
- 9. areas that will be temporarily or permanently stabilized on the site

4. Spill Prevention and Response Plan

Describe the spill prevention and control plan to include ways to reduce the chance of spills, stop the source of spills, contain and cleanup spills, dispose of materials contaminated by spills, and train personnel responsible for spill prevention and control. Additionally, fill in all BLUE fields below.

Spill Plan:

Store materials in a location to prevent the possibility of a spill. Should a spill happen follow the procedures of the manufacture. If the spill is of another issue then the proper entity should be contacted and the necessary processes taken. See EPA's Spill Prevention and Control Plan BMP if necessary.

www.epa.gov/npdes/stormwater/menuofbmps/construciton/spill_control htp://www.epa.gov/npdes/stormwater/menuofbmps

Any discharges in 24 hours equal to or in excess of the reportable quantities listed in 40 CFR 117, 40 CFR 110, and 40 CFR 302 will be reported to the National Response Center and the Division of Water Quality (DWQ) as soon as practical after knowledge of the spill is known to the permittee. The permittee shall submit within 14 calendar days of knowledge of the release a written description of: the release (including the type and estimate of the amount of material released), the date that such release occurred, the circumstances leading to the release, and measures taken and/or planned to be taken to the Division of Water Quality (DWQ), 288 North 1460 West, P.O. Box 144870, Salt Lake City, Utah 84114-4870. The Storm Water Pollution Prevention Plan must be modified within14 calendar days of knowledge of the release to provide a description of the release, the circumstances leading to the release, and the date of the release. In addition, the plan must be reviewed to identify measures to prevent the reoccurrence of such releases and to respond to such releases, and the plan must be modified where appropriate.

Agency Phone Number

National Response Center	(800) 424-8802
Division of Water Quality (DWQ) 24-Hr Reporting	(801) 538-6146; (801) 536-4123
Utah Department of Health Emergency Response	(801) 580-6681
Local Fire Department	801 782 3580

Minimum spill quantities requiring reporting:

Material	Media Released To	Reportable Quantity
Engine oil, fuel, hydraulic & brake fluid	Land	25 gallons
Paints, solvents, thinners	Land	100 lbs (13 gallons)
Engine oil, fuel, hydraulic & brake fluid	Water	Visible Sheen
Refrigerant	Air	1 lb
Antifreeze, battery acid, gasoline, engine degreasers	Air, Land, Water	100 lbs (13 gallons)

Emphasis to:

1st Priority: Protect all people (including onsite staff)

2nd Priority: Protect equipment and property

3rd Priority: Protect the environment

- 1. Make sure the spill area is safe to enter and that it does not pose an immediate threat to health or safety of any person.
- 2. Check for hazards (flammable material, noxious fumes, cause of spill) if flammable liquid, turn off engines and nearby electrical equipment. If serious hazards are present leave area and call 911. LARGE SPILLS ARE LIKELY TO PRESENT A HAZARD.
- 3. Stop the spill source and contain flowing spills immediately with spill kits, dirt or other material that will achieve containment.
- 4. Call co-workers and supervisor for assistance and to make them aware of the spill and potential dangers
- 5. If spilled material has entered a storm sewer, regardless of containment; contact the City Stormwater Division.
- 6. Cleanup all spills (flowing or non-flowing) immediately following containment. Clean up spilled material according to manufacturer specifications, for liquid spills use absorbent materials AND DO NOT FLUSH AREA WITH WATER.
- 7. Properly dispose of cleaning materials and used absorbent material according to manufacturer specifications.
- 8. Report the reportable quantity to the Weber Morgan Health Department.

Emergency Numbers

Utah Hazmat Response Officer 24 hrs	(801)-538-3745
City Police Department	801 629-8221
City Engineering Division	801 399 8374

5. SWPPP, Inspections and Corrective Action Reports

Inspection Schedule and Procedures: The permit requires inspections once a week (see permit Part 3). You must list and provide details of your BMPs in Appendix L. Inspection reports require reporting on BMPs and how effective they are. You may be required to maintain, modify, remove, or apply/install more or different BMPs to control pollutants on the site. Please number your BMPs in Appendix L and refer to those numbers on your inspection reports and corrective action reports when you inspect or report on them.

Describe the general procedures for correcting problems when they are identified. Include responsible staff and time frames for making corrections:

Within a day or so of discovering the occurrence of a storm water or pollution control problem at your site, you must make an entry in a report/log or other devise for monitoring corrective action of the following: a: What condition was identified at your site that required corrective action (BMPs needed or in need of altering or repairing.

b: The date and time the condition was identified and how it was identified (noticed it needed maintenance, Inspection)

Carson Young is the Responsible Staff and he will Immediately take all reasonable steps to minimize or prevent the discharge of pollutants until a permanent solution for the problem is installed and made operational. See Part 5.2 or the General Permit

Corrective Actions: All corrective actions must be logged using the "Correction Action Log" attached in Appendix F. The log should be filled out completely for each corrective action.

Corrective Actions: All corrective actions must be logged using the "Correction Action Log" attached in Appendix F. The log should be filled out completely for each corrective action.

6. Changes to the SWPPP

All changes to this SWPPP must be logged in the "Amendment Log" in Appendix G. The log should be filled out completely for each amendment to the SWPPP.

7. Record Keeping

The following items should be kept at the project site available for inspectors to review:

1. Dates of grading, construction activity, and stabilization

- 2. A copy of the construction general permit (Appendix C)
- 3. The signed and certified NOI form (Appendix D)
- 4. Inspection reports (Appendix E)

8. Delegation of Authority (if any)

Duly Authorized Representatives or Positions:

Company/

Solitude Builders LLC.

Organization:

Name Carson Young

Position General Contractor

Address 2068 E 5950 N

City Liberty

State: Ut

Zip: 84310

Telephone (801 452 5020

Fax/

(XXX) XXX-XXXX

Email:

Note: Any additional information (i.e. memoranda, agreements, etc.) should be attached in Appendix H.

9. Discharge Information

Does your project/site discharge storm water into a Municipal Separate Storm Sewer System (MS4)?

x Yes

□ No

MS4 receiving the discharge from the construction project:Unincorporated Weber County

Receiving Waters (look up http://wq.deq.utah.gov to identify your receiving water body)

Enter the name(s) of the first surface water(s) that receives stormwater directly from your site and/or from the MS4 listed above. Note: multiple rows provided in the case that your site has more than one point of discharge in which each flows to different surface waters.

- 1. Strom Drain
- 2. Wolf Creek
- 3. North Fork
- 4. PineVeiw

Impaired Waters (refer to http://wq.deq.utah.gov in the left hand column to determine status of receiving water body).

Select any impaired surface water(s) that your site will discharge to, either directly or through the MS4 selected above.

Stormwater Pollution Prevention Plan Template (SWPPP) Common Plan Permit

Impaired Surface Water	Is this surface water impaired?		Pollutant(s) causing the impairment	be	TMDL en leted?	Pollutant(s) for which there is a TMDL	
Pineview Reservoir	x Yes	□ No	Dissolved Oxygen, Phosphorus, Temp.	x Yes	□ No	Nitrogen&Phospho	
5	□ Yes	□ No		□ Yes	□ No	Click here to enter text.	

10. Certification and Notification

I, Carson Young, certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Construction Operator:

This SWPPP should be signed and certified by the construction operator(s). Attach certifications in Appendix H.



SWPPP Appendices

Ensure the following documentation is attached to the SWPPP:

Appendix A: General Location Map

Appendix B: SWPPP Site Maps

Appendix C: Construction General Permit Regulation

Appendix D: Acknowledgement Letter from City Name Here.

Appendix E: Inspection Reports

Appendix F: Corrective Action Log

Appendix G: SWPPP Amendment Log

Appendix H: Certifications, Agreements, and Delegation of Authority


Appendix I: Grading and Stabilization Activities Log

Appendix J: Construction Plans

Appendix K: Additional Information (i.e. permits such as local permits, dewatering, stream alteration, wetland, and out of date SWPPP documents, etc.)

Appendix L: BMP Specifications and Details (label BMPs to match the sections identified in this document.)

APPENDIX B: SWPPP Site Maps

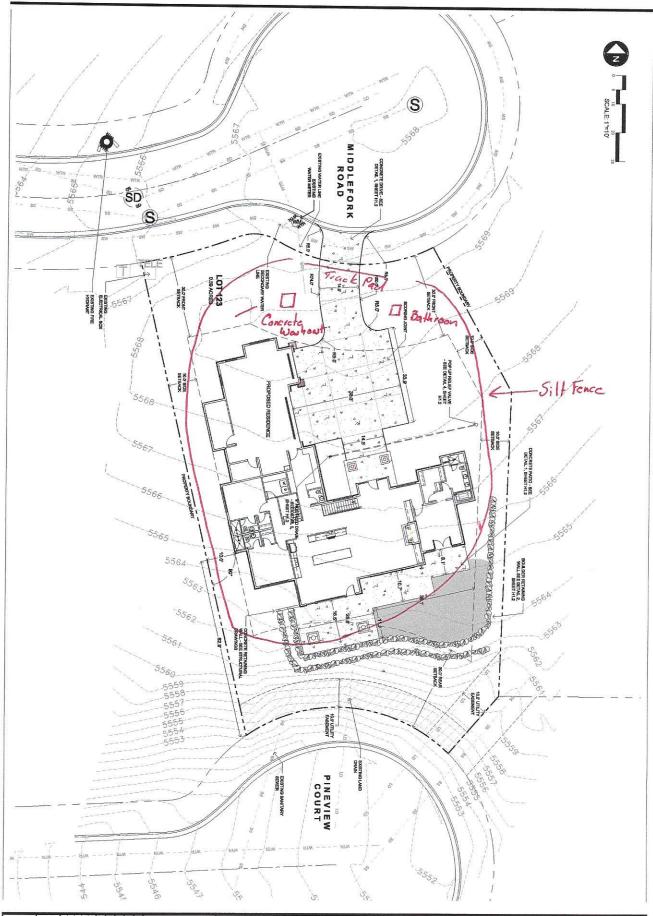

MEGROZ RESIDENCE
---- MIDDLEFORK ROAD, EDEN, UT 84310
LOT 123, WOLF CREEK RESORT WEBER COUNTY, UT



Stormwater Pollution Prevention Plan

1-Distarbed Area 4000 sqft

2-Solitade Bailder responsible for Site conditions

Carson Joung
Solitude Bailders

861 452-5620

3-Storm Water Pollution Prevention Plan

4-Execusted Materials Vill be hauled off site

5-Concrete Wash out Located on Site Plan

6-Portable Toich Located on Site Plan

7-Construction Access Located on Site Plan With Track out Pad

8-Track out Pad Street will be Cleaned by Solitade Bailders

9-Silt Fence as needed

10-New home Shown on Site Plan

APPENDIX C: Co		24.000		
39 *				
×				
	-			

APPENDIX D: Acknowl	edgement Letter from Cit	y Name Here.	
		77.51	1

General Permit for Storm Water Discharges from Construction Activities

STATE OF UTAH, DEPARTMENT OF ENVIRONMENTAL QUALITY, DIVISION OF WATER QUALITY

General Storm Water Permit for Construction Activity
Connected with Single Lot Housing Projects
Utah Pollution Discharge Elimination System Permit No. UTRH00000
(Common Plan Permit)

This Permit is issued in compliance with the provisions of the Utah Water Quality Act (Utah Code Annotated 19-5, as amended) the federal Water Pollution Control Act (33 United States 1251 et. seq., as amended by the Water Quality Act of 1987, Public Law 100-4), and the rules and Regulations made pursuant to those statutes.

This permit applies to "construction activity" for a single lot disturbing a total of one acre or less and for construction activities related to residential dwellings. A single lot covered by this permit is part of a common plan of development or sale (see definitions in Part 6).

Issuance of this permit does not authorize any permittee to violate water quality standards. The permittee shall develop best management practices (BMPs) and engage in activities that will protect water quality during the construction project.

This permit shall become effective on February 1, 2016.

This permit and the authorization to discharge expire at midnight on January 31, 2021.

Signed this Oday of January, 2016

Walter L. Baker, P.E.

Director

DWQ-2016-00208

Jy

TABLE OF CONTENTS

1.	COV	ERAGE UNDER THIS PERMIT	1
	1.1.	Coverage Limitations	1
	1.2.	Discharges Allowed	1
	1.3.	Non-Storm Water Discharges.	1
	1.4.	How to Obtain Permit Coverage	1
	1.5.	Signature on the NOI	2
	1.6.	Permit Renewal	2
	1.7.	Start and end of Permit Coverage	2
	1.8.	Notice of Termination	3
	1.9.	Water Quality	3
	1.10	Requirement to Post a Notice of Permit Coverage	3
2.	POL	LUTION PREVENTION REQUIREMENTS	4
		Structural Controls	
		Protection of Critical or Sensitive Areas	
		Managing the Site to Minimize Sediment Transport Off Site	
		Good Housekeeping Measures	
		Soil Compaction/Top Soil	
		Stabilization Requirement	
		Construction Dewatering	
		Pollution Prevention Measures	
		Prohibited Discharges	
3.	SELI	-INSPECTION REQUIREMENTS	9
	3.1.	Inspector Qualifications.	9
	3.2.	<u>Self-Inspections</u>	9
	<i>3.3.</i>	Weekly Self-Inspection Requirements	9
	3.4.	Weekly Inspection Reports	.0
	3.5.	Corrective Action	0
Λ	CTO	DNA WATER DOLLLITION PREVENTION DLAN (SW/DDD)	1

4.	1. SWPPP Requirement	11
4	2. <u>Contents of a SWPPP</u>	11
5. \$1	ANDARD PERMIT CONDITIONS	14
5	1. Duty to Comply	14
5.2	2. <u>Duty to Reapply</u>	14
5.3	3. <u>Need to Halt or Reduce Activity not a Defense</u>	14
5.4	4. <u>Duty to Mitigate</u>	14
5.5	5. <u>Duty to Provide Information</u>	14
5.6	5. <u>Other Information</u>	14
5.7	7. Oil and Hazardous Substance Liability	15
5.8	3. Property Rights	15
5.9	9. <u>Severability</u>	15
5.1	10. Record Retention.	15
5.1	11. Addresses	15
5.1	12. <u>State Laws</u>	15
5.1	13. Proper Operation and Maintenance	15
5.1	4. Inspection and Entry.	15
5.1	5. <u>Reopener Clause</u>	16
5.1	6. <u>Signatory Requirements</u>	16
6. DE	FINITIONS	18

- 1. COVERAGE UNDER THIS PERMIT. Conditions for coverage under this permit.
 - 1.1. <u>Coverage Limitations</u>. A project site (see definition of a project site in Part 6) is eligible for this permit if it meets the following requirements:
 - 1.1.1. It is found within the State of Utah but is not in Indian Country,
 - 1.1.2. The construction activity is related to residential building on an individual lot or parcel.
 - 1.1.3. It disturbs a total of one acre or less over the duration of the construction project,
 - 1.1.4. Multiple site coverage:
 - 1.1.4.a. This permit may apply to multiple lots with the contingency that each lot be covered under a different permit tracking number (separate permit coverage for each lot). Lots do not necessarily need to be located within the same sub-division.
 - 1.1.4.b. If multiple lot coverage is desired under one permit, it may be obtained under the General Permit for Discharges from UPDES Permit No. UTRC00000. Multiple lots may be covered under one tracking number (one permit coverage) provided that UTRC00000 is the controlling permit, and all lots covered under that tracking number are within the same sub-division.
 - 1.2. <u>Discharges Allowed</u>. This permit allows discharges of storm water from construction activity at a project site, provided the storm water discharge meets the requirements within this permit.
 - 1.3. Non-Storm Water Discharges. Other non-storm water discharges that are allowed are:
 - 1.3.1. Flushings from potable or irrigation water sources where they have not been used for a washing or cleaning activity;
 - 1.3.2. Water used for dust control;
 - 1.3.3. Spring water and groundwater that have not been soiled with sediment or other pollutants from construction activity;
 - 1.3.4. Emergency fire-fighting activities, and;
 - 1.3.5. Footing drains that have not been soiled from construction activity.
 - 1.4. How to Obtain Permit Coverage. The permit may be obtained online at the Utah Department of Environmental Quality (DEQ) UPDES Permits website at http://www.waterquality.utah.gov/UPDES/stormwatercon.htm. Click on "Application for a Storm Water Permit". Create an account, or if an account has already been created, proceed with providing the information requested. The notice of intent (NOI) for this permit is the same NOI that is used for the UTRC00000 permit. To complete the application process the permittee must pay a permit fee. The NOI may be filled out electronically using the online permit application system. The NOI can also be submitted using a paper form obtained from the same website cited above along with the permit fee. The paper form and fee can either be hand delivered to Utah Division of Water Quality [DWQ], 195 North 1950 West, Salt Lake City, Utah, 3rd floor in the MASOB building, or mailed to DWQ, P.O. Box 144870, Salt Lake City, Utah 84114-4870. When a party receives coverage under the permit, they will receive a permit

- tracking number and the opportunity to copy the NOI for "proof of coverage." A copy of this permit may be downloaded from the DEQ website at http://www.deq.utah.gov/Permits/water/updes/stormwatercon.htm.
- 1.5. <u>Signature on the NOI</u>. The owner and the general contractor, which in some cases could be the same party, must sign the paper copy of the NOI (see 5.16.1.a) and place it in the storm water pollution prevention plan (SWPPP) (see 4.2.8).
- 1.6. <u>Permit Renewal</u>. This permit must be renewed yearly on the anniversary date of the original permit application. This is done by logging onto the account created at the time of NOI application, refreshing the information on the NOI, and paying the yearly permit fee.
- 1.7. Start and end of Permit Coverage. Permit coverage begins immediately upon completion and submission of an NOI and the permit fee. If the NOI is submitted electronically on-line permit coverage begins on that day. If the NOI is submitted by mail permit coverage begins when the NOI is received and entered into the on-line data base by DWQ staff. For projects within the jurisdiction of a regulated MS4 (see definitions in Part 6; the list of regulated MS4's is found on http://www.deq.utah.gov/Permits/water/updes/stormwatermun.htm), the permittee must also notify and receive approval for the project from the regulated MS4 having jurisdiction before the project may commence (see 4.2.10.). The permit fee is an annual fee that must be paid yearly on the anniversary date of permit issuance. The permit will remain effective until or unless any of the following occurs:
 - 1.7.1. The permittee completes the notice of termination (NOT) process, as outlined in section 1.8,
 - 1.7.2. The permittee fails to submit the yearly permit fee,
 - 1.7.3. Aside from permit coverage, which may be renewed annually by the permittee, as needed, this general permit expires every 5 years and normally is renewed through a public notice process by DWQ. In the event that the permit nears the end of its 5 year cycle, and the year of permit coverage for a construction site extends beyond the expiration date for the permit, the permittee must request continuing coverage through the permit renewal process. Otherwise permit coverage for a construction site will terminate when the general permit expires. Renewal of permit coverage can be done in the online electronic storm water data base up to 12 months prior to the expiration of the permit, or by letter received by DWQ before the expiration date of the specific permit coverage in question where concurrently all entries in the NOI can be updated as needed.
 - 1.7.3.a. If a renewal permit has been issued and is in place at the expiration date of this permit, this permit will terminate and coverage under the renewed permit will begin on the expiration date unless 1.7.1 has been invoked by the permittee.
 - 1.7.3.b. If a renewal permit has not been issued, this permit will be administratively extended until a renewal permit is issued or it is determined that this permit will not be continued. If a renewal permit is issued, and the permittee indicated a desire for continuing coverage under the new permit, coverage

will continue for the permittee under the new permit coverage unless 1.7.1 is invoked. If the permit is discontinued, the permittee must continue coverage under another general permit or an individual permit.

- 1.7.4. Coverage under this permit is rescinded or revoked for administrative reasons. In this case, the permittee will be notified in writing from the Director and will be required to apply for coverage under a different general or individual UPDES permit. This permit is terminated on the day coverage under another permit begins.
- 1.8. Notice of Termination. The permittee must terminate the permit by submitting an NOT when the project is completed. The NOT must be filed and retained for 3 years after the permit has been terminated (see 3.7). To terminate the permit, the permittee must comply with either 1.8.1 or 1.8.2, outlined below, and must comply with 1.8.3 if the project is within the jurisdiction of a regulated MS4 (see http://www.deq.utah.gov/Permits/water/updes/stormwatermun.htm for regulated MS4s):
 - 1.8.1. The landscaping is completed and the site meets "final stabilization" requirements (see part 6, definitions, for final stabilization).
 - 1.8.2. When a project (residential building) is completed but 'final stabilization' is not established, the building must be in process of being sold and ready for homeowners to take possession. If built by the homeowners, they must be in the process of moving in or already have moved in the house. The lot must have perimeter controls on downslope boundaries and surface stabilization controls on all surfaces that are 20 % (1 to 5 slope, or 11.3 derees) or greater to prevent erosion and soil migration offsite;
 - 1.8.3. The permittee must submit a paper copy of a NOT form to the MS4 of jurisdiction and schedule a final inspection (with the MS4). Termination is complete upon approval of the final inspection from the local MS4, or from DWQ if outside the jurisdiction of a regulated MS4.
- 1.9. Water Quality: Through the design of appropriate BMPs, it is expected that the permittee will achieve compliance with water-quality standards. If additional information becomes available indicating a project site is causing or is contributing to a violation of water quality standards or an existing total maximum daily load (TMDL), coverage under this permit may be revoked or rescinded, and the permittee may be required to get coverage under an individual UPDES permit or another UPDES general permit. If this occurs, the owner and the general contractor will be notified in writing by the Director and given instructions on how they must proceed.
- 1.10. Requirement to Post a Notice of Permit Coverage. The permittee must post a sign at the project site that includes the UPDES Permit tracking number, owner or general contractor contact name, a phone number for the owner or general contractor, an email address for the owner or general contractor, and in the case of an electronic SWPPP, a web address or information on how to access the electronic SWPPP. The notice must be posted with lettering large enough to be readable from a public right-of-way.

2. POLLUTION PREVENTION REQUIREMENTS

- 2.1. Structural Controls. Minimize sediment transport off the site as follows:
 - 2.1.1. Stockpiled Material. Stockpiled material must not be stored on an impervious surface, except a material that will not be transported with precipitation, such as two-inch graded and washed gravel, unless it will be permanently placed and the holding area will be swept clean the same day it is dropped. If stored temporarily for more than a day, it must be placed as far as feasibly possible from roads or other impervious surfaces, storm water inlets, or water bodies, and with stockpile perimeter runoff controls utilized.
 - 2.1.2. Perimeter Controls. Perimeter controls such as silt fences, straw wattles, other filter berms, cut back curbs, vegetative buffers, etc., must be properly placed on the downslope sides of the project to prevent sediment from leaving the site during a storm event. As perimeter controls become loaded to 1/3 of capacity, they must be cleaned.
 - 2.1.3. Inlet Protection. Storm-drain inlets on the project site and on adjacent roads immediately down gradient from the site must be protected if they receive drainage from the active constructionsite. Protection may be, but is not limited to, rock wattles, sand bags, proprietary devices, or other. Rock wattles and sand bags are not advised for use in winter because they can be destroyed or removed by snow plows.
- 2.2. <u>Protection of Critical or Sensitive Areas</u>: Critical or sensitive areas such as preservation of the drip line around trees, wetlands, buffer zones by water bodies, etc., must be separated and isolated by clearly marking the areas with environmental fencing.
- 2.3. Managing the Site to Minimize Sediment Transport Offsite.
 - 2.3.1. The total area of soil disturbance at any one time must be minimized by disturbing only the area necessary to complete that stage of construction in the construction process.
 - 2.3.2. Soil disturbances on steep slopes must be minimized. For purposes of this permit a steep slope is 70% (or 1 to 1.66, or 35 degrees), or greater. This means avoiding a disturbance of soils on steep slopes or if disturbing the soil surface is necessary providing a robust surface stabilizing cover (such as geomats, environmental blankets, or other robust slope stabilizing control) to prevent erosion.
 - 2.3.3. Storm water volume and velocity must be controlled to minimize soil erosion and sediment transport by methods such as allowing or not obstructing infiltration and using velocity-control devices to reduce energy in runoff flowing on slopes.
 - 2.3.4. Storm water discharges leaving the site, including both peak flowrates and total storm water volume, must be controlled to minimize channel and stream-bank erosion and scour in the immediate vicinity of discharge points. This may be accomplished using experience, estimates, and good judgement; unless unusual or extraordinary site conditions present a potential for excessive erosion, hillside/impoundment collapse, environmental/safety hazards, or other site problems; for which a professional engineer must be consulted.

2.3.5. Thirty-Foot Vegetative Buffer. If a waterbody is adjacent to, within 30 feet from, or passing through the project boundaries, a 30-foot natural buffer between the waterbody and construction activity must be provided. If a 30-foot natural buffer cannot be provided, a substitute control measure equivalent to the 30-foot buffer must be provided, or the SWPPP must contain an explanation why neither is feasible. If it is not feasible to maintain a 30-foot natural buffer, as much natural buffer as is possible must be preserved and coupled with placement of additional erosion and sediment controls designed, implemented, and maintained to substitute and be equivalent to the 30-foot natural buffer.

The requirement for a natural buffer or substitute controls does not apply to any area outside of the project boundaries, but if a waterbody is within, for example, 20 feet from the project boundary, there must be 10 feet of natural vegetative buffer or substitute controls, or if within 25feet from the project boundary, there must be 5 feet of natural vegetative buffer or substitute controls, and so forth.

- 2.3.5.a. Substitution for a natural buffer should be calculated with models such as USDA's RUSLE2 or WEPP, or by using SEDCAD, SEDIMOT, or other similar models. In lieu of using a model for calculation of a substitution buffer, the permittee shall deploy the following:
 - 2.3.5.a.i. For every full 9 feet of natural buffer that is not provided on slopes up to 10 percent, one row of an effective perimeter control, such as a silt fence, staked straw wattle, proprietary or other filter berm, or other perimeter control, must be properly placed. For example, if only 15 feet of natural buffer can be provided, the permittee will substitute one row of a perimeter control in addition to the 15 feet of natural buffer to make up for the 15 feet of buffer that could not be preserved.
 - 2.3.5.a.ii. In addition to the requirements above for substitutions in place of the 30-foot natural buffer, on slopes between 10 percent and 30 percent, five feet of surface stabilization must be placed down gradient of and between each perimeter control substituted. For slopes steeper than 30 percent, 6 feet of surface stabilization must be placed downgradient of and between each perimeter control substituted, such as mulch, hydromulch, wood chips, bark, compost, erosion mat, etc., but excluding tackifiers.
- 2.4. Good Housekeeping Measures. The permittee must address the following:
 - 2.4.1. Track Out. Track-out pads (see definitions) and or rumble strips (see definitions) must be used to prevent dirt/mud tracked on streets as vehicles leave the site. If traffic onto and off the site is not frequent, a site operator may impose a blanket prohibition of vehicle traffic onto the site, allowing for the occasions to deliver and unload, but afterwards providing sweeping and/or cleaning of tracked out dirt (keep in mind that vehicles leaving a muddy site with no track out protection can track mud for several

- blocks the operator is liable for all track out from the site except for a dirt stain after sweeping see note after 3.2.2.). Dirt or mud tracked out on the street must <u>not</u> be washed or hosed into a storm drain. Tracked out mud or dirt on the street must be swept and/or scraped up as needed every day (see 3.2.2).
- 2.4.2. Curb Ramps: This permit prohibits the intentional placement of dirt and/or mud on paved streets or sidewalks. Curb ramps may be crushed rock, wood or steel ramps, or another material that does not wash away with storm water.
- 2.4.3. Waste and Debris. The site must be cleaned of waste and debris daily (see daily self-inspection 3.2.2). Waste and debris must be contained and secured adequately to prevent scattering from wind until it is removed from the site and disposed of properly.
- 2.4.4. Portable Toilet. Portable toilets must be tied down, staked down, or secured using other measures to prevent turn over, and they must be placed away from a road gutter, storm water inlet, or waterbody.
- 2.4.5. Washing of Concrete, Stucco, and Paint Equipment. A plastic film-lined pit or sealed container must be provided for washout of equipment used for concrete, stucco, and water-based paint. After completion of concrete, stucco, and paint tasks, the permittee must dispose of the waste by drying and sending solids to a landfill. Oil-based paint cleanout must be done in containers, taken off-site, and disposed of separately.
- 2.5. <u>Soil Compaction/Top Soil</u>. Topsoil must be preserved and placed on areas to be landscaped or areas planned for receiving vegetative cover, unless infeasible. Soil compaction must be minimized on areas that will not be used for support of structural elements such as roads, parking areas, structures, etc., unless infeasible.
- 2.6. Stabilization Requirement. Stabilization requirements are as follows:
 - 2.6.1. Stabilization requirements for areas that receive 20 inches of rainfall annually or greater: Stabilization of disturbed areas must, at a minimum, be initiated immediately whenever any clearing, grading, excavating or other earth disturbing activities have permanently ceased on any portion of the site or have temporarily ceased on any portion of the site for greater than 14 calendar days. Stabilization can be sodding, planting, application of mulch (wood chips, rock, gravel, bark, compost, cat tracking on straw, hydromulch, etc.), application of geotextiles or erosion blankets, application of a tackifier, seeding (including preparation for germination and growth), a combination of these methods, or other method.
 - 2.6.2. Stabilization or equivalent requirements for arid and semi-arid areas (areas receiving less than 20 inches of rainfall annually): Stabilization for visually flat areas is not required (roughly up to 5 percent, 1 to 20 slope, or 2.3 degrees slope). Areas with slopes up to roughly 20 percent (1 to 5 slope or 11.3 degrees) must have, at minimum, velocity-control devices in every area where storm water collects and flows, spaced close enough across the flow to stop erosion (see also 2.3.3). Soil surface stabilization such as sodding, planting, hydromulch, compost, bark, cat tracking on straw, gravel,

geotextiles, erosion blankets, or other stabilization methods is required on all other sloped areas, increasing the robust nature of stabilizing cover commensurately with increasingly steeper slopes.

- 2.6.3. Permanent Stabilization for Arid areas.
 - 2.6.3.a. In addition to requirements above (see 2.6.2), permanent stabilization requires seeding on all areas that are not covered with permanent stabilization elements or structural elements such as building structure or pavement, or that are engineered or intended for structural purposes like graveled parking or dirt roads.
 - 2.6.3.b. Disturbed areas on projects located outside of populated and developed areas and where no irrigation water is available and where future periodic landscaping maintenance is not planned must be reclaimed with a seed mix of plants indigenous to the area or tolerant to the local climatic conditions that does not include invasive species. Velocity-control devices may be permanent or temporary. If velocity-control devices are intended for temporary use, they must be biodegradable and designed durable enough to withstand extreme weather.
- 2.7. Construction Dewatering. Construction dewatering can occur onsite without an additional UPDES permit if it is infiltrated or contained onsite and is not discharged offsite. Otherwise, construction dewatering discharges must be permitted under the General Permit for Construction Dewatering and Hydrostatic Testing UPDES Permit UTG070000, which can be obtained online through submittal of an NOI at https://secure.utah.gov/waterquality.
- 2.8. <u>Pollution Prevention Measures</u>. The permittee must design, install, implement, and maintain effective pollution prevention measures to minimize the discharge of pollutants. At a minimum, such measures must address the following:
 - 2.8.1. Vehicle, Wheel, and Other Washing. Minimize the discharge of pollutants from equipment and vehicle washing, wheel-wash water, and other wash waters. Wash waters must be treated in a sediment basin or alternative control that provides equivalent or better treatment prior to discharge
 - 2.8.2. Exposure to Pollutants. Minimize the exposure of building materials, building products, construction wastes, trash (see 2.4.3), landscape materials, fertilizers, pesticides, herbicides, detergents, sanitary waste (see 2.4.4), and other materials present on the site to precipitation and to storm water. Minimization of exposure is not required in cases where the exposure to precipitation and to storm water will not result in a discharge of pollutants, or where exposure of a specific material or product poses little risk of storm water contamination (e.g., final products and materials intended for outdoor use).
 - 2.8.3. Leaks and Spills. Minimize the discharge of pollutants from spills and leaks and implement chemical spill and leak prevention and response procedures.
- 2.9. Prohibited Discharges. The following discharges are prohibited:
 - 2.9.1. Wastewater from washout or cutting of concrete (see 2.4.5),

- 2.9.2. Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction materials (see 2.4.5),
- 2.9.3. Fuels, oils, or other pollutants used in vehicle and equipment operation and maintenance,
- 2.9.4. Soaps or solvents used in vehicle and equipment washing.

3. SELF-INSPECTION REQUIREMENTS.

- 3.1. <u>Inspector Qualifications</u>. Weekly inspections (see 3.2.1 below) must be done by a qualified person. A qualified person means a person knowledgeable in the principles and practices of erosion and sediment control that possesses the skills to:
 - 3.1.1. Assess conditions at the construction site that could impact storm water quality,
 - 3.1.2. Assess the effectiveness of a storm water control measure selected to control the quality of storm water discharges from the construction activity.

3.2. Self-Inspections.

- 3.2.1. Weekly Self Inspections: Self-inspections must occur every 7 days. A written report is required (see 3.4).
- 3.2.2. Daily Site Check: Each day of construction activity, the site must be inspected for dirt in the street and trash on the site. Streets must be swept clean (see note below), if soiled. Dirt must be removed off the street (not swept or washed into the storm drain system). Trash on the site must be picked up and disposed of into trash containers (see 2.4.3.) or disposed of off-site (e.g., municipal/private garbage collection service or construction waste landfill). Sub-contractors must be held responsible by the permit holder to perform these duties in accordance with this paragraph for the activities they are contracted to perform. A written report is not required, however the operator will keep a daily log (for the active construction days) listing the initials of the person doing the site check.

Note: Swept clean means sweeping and scraping. Scraping if there is dirt left behind that is crusted and that sweeping will not pick up. This does not mean removing the microscopic layer of dust or the minute amounts of dirt in the cracks and crevices of the surface left behind staining the pavement.

3.3. Weekly Self-Inspection Requirements.

- 3.3.1. Areas to check include the following:
 - 3.3.1.a. Areas that have been cleared, graded, or excavated that are not stabilized,
 - 3.3.1.b. All storm water control measures, including perimeter controls,
 - 3.3.1.c. Material piles, waste-disposal containers, sanitary facilities, loose trash, litter, washout areas, portable toilets, track out pad, egress points (if any), etc.,
 - 3.3.1.d. Storm water conveyances through the site, treatment areas, and drainages,
 - 3.3.1.e. All storm water discharge points, street gutters, storm water inlets,
 - 3.3.1.f. Areas that have been temporarily stabilized,
 - 3.3.1.g. Areas that have been permanently stabilized and are completed do not need further inspections.
- 3.3.2. Items to check include the following:
 - 3.3.2.a. All erosion and sediment controls and other pollution prevention controls

have been installed, are operational, and are working as intended to minimize pollutant discharges. Determine if any controls need to be replaced, repaired, or maintained.

- 3.3.2.b. Identify any locations where new or modified storm water controls are necessary.
- 3.3.2.c. Signs of visible erosion and sedimentation (i.e., sediment deposits) that have occurred and are attributable to discharges from your site,
- 3.4. <u>Weekly Inspection Reports</u>. The weekly self-inspection report must be written within 24 hours of inspection and must include:
 - 3.4.1. The initials of the person doing the inspection,
 - 3.4.2. The date of the inspection,
 - 3.4.3. The weather during the inspection,
 - 3.4.4. The problems that were found needing correction (as they pertain to 3.3.1 and 3.3.2 above).
 - 3.4.5. The date when corrective action is completed,
 - 3.4.6. All self-inspection reports must be filed with other permit records regarding the permit. Inspection reports must be available during an oversight inspection.
- 3.5. Corrective Action: Corrective action must be completed before the next weekly inspection.
- 3.6. <u>Inspections by an Oversight Authority</u>. A copy of an oversight inspection report must be filed and be available for review during other oversight inspections.
- 3.7. <u>Record Keeping</u>. Records regarding this permit, the NOI, the NOT, the SWPPP, inspection reports, other related information and documents must be preserved for 3 years after the submission of the NOT (see 5.10).

- 4. STORM WATER POLLUTION PREVENTION PLAN (SWPPP).
 - 4.1. <u>SWPPP Requirement</u>. The permittee must prepare a SWPPP before the NOI for the project is submitted. The SWPPP must address all the applicable requirements in Part 2.
 - 4.1.1. SWPPP Site Design. The design, installation, and maintenance of erosion and sediment controls must address factors such as the amount, frequency, intensity and duration of precipitation; the nature of resulting storm water runoff; and soil characteristics, including the range of soil particle sizes expected to be present onsite. These may be accomplished using experience, estimates, and good judgement, unless unusual or extraordinary site conditions create hazards for which a professional engineer must be consulted.
 - 4.1.2. Surface Outlets: When discharging from basins and impoundments, utilize outlet structures that withdraw water from the surface, unless infeasible.
 - 4.2. Contents of a SWPPP. A SWPPP must contain the following:
 - 4.2.1. *Contacts*. The contacts for the site with contact information (name, address, telephone, email) including owner, general contractor, and any other party that significantly affects the implementation of the SWPPP or has responsibilities over the SWPPP.
 - 4.2.2. Sequence and Estimated Dates of Construction Activities. Listed in the sequence with estimated dates including the following:
 - 4.2.2.a. Start and end of excavation activities, initial excavation, backfill excavation and final grading,
 - 4.2.2.b. Any temporary or permanent cessation of earth-disturbing activities,
 - 4.2.2.c. Start and end of landscaping if this is done as part of the construction activity before the home is sold.
 - 4.2.3. Site Map or Chart. A site map may be hand drawn (as close to scale as possible) or may be a copy of an architect drawing including the following information:
 - 4.2.3.a. Boundaries of the property,
 - 4.2.3.b. Boundaries of soil surface disturbances, including any outside the boundaries of the property,
 - 4.2.3.c. Slopes, including areas of steep slopes,
 - 4.2.3.d. Locations of stockpiles of soils, storage of construction materials, portable toilets, trash containers, concrete washout pits or containers, egress points, and track out pads,
 - 4.2.3.e. Waterbodies, wetlands, and natural buffer areas,
 - 4.2.3.f. Locations and types of BMPs or storm water control measures for the control and/or treatment of storm water flowing onto, through, and/or offsite,
 - 4.2.3.g. Locations of storm water inlets, storm water discharge points going off site,

- 4.2.3.h. Areas that will be temporarily or permanently stabilized during the construction period.
- 4.2.4. Thirty-Foot Natural Buffer. The SWPPP must show the dimensions and placement of the 30-foot natural buffer, the substitute control measures, or a detailed explanation of why a natural buffer or substitute control measure could not be applied.
- 4.2.5. Pollutants. A list of construction site pollutants including the pollutant-generating activity, and an inventory of pollutants for each pollutant generating activity (e.g., paints, solvents, form oil, fuels, and other chemicals; applications, materials, and liquids that if released could pollute storm water).
- 4.2.6. Waste Management. Waste management procedures including soil removal, clearing debris removal, demolition removal, trash disposal, construction-waste disposal, and sanitary-waste disposal.
- 4.2.7. Training. The permittee will ensure that each subcontractor or utility provider is aware of their responsibilities for keeping soil on the site and preventing pollution. The permittee must keep in mind that they are responsible for and may be issued fines for poor performances by their subcontractors and utility providers. Consideration will be given if the permittee can document when and what instructions were given to the subordinate party.
- 4.2.8. NOI and Permit. The SWPPP must contain a copy of this permit and a copy of the NOI for the project.
- 4.2.9. SWPPP Signature and Certification. The SWPPP must be signed and certified by both the Owner and the General Contractor in accordance with 5.16.1.a.
- 4.2.10. MS4 Approval of Project. For areas where projects are within a regulated MS4's jurisdiction (see definitions in Part 6; the list of regulated MS4's is found on http://www.deq.utah.gov/Permits/water/updes/stormwatermun.htm), the SWPPP must contain the signature and date of the MS4 reviewer who has approved the proposed project for construction (see 1.7.).
- 4.2.11. Availability of the SWPPP. The SWPPP must be available at the construction site covered under this permit during onsite construction activity, unless the SWPPP is available online. If the SWPPP is available online there must be a sign (see 1.10) that describes where the SWPPP can be accessed online. The SWPPP is a plan for the site, and workers must be able to refer to the SWPPP and update it as needed to manage the site (including SWPPPs found on the internet). The SWPPP is not required to be on the site when construction workers leave for the day or when there is no activity occurring on the site, but at all times there must be posted contact information where the SWPPP can be obtained (see Part 1.10). The SWPPP must be made available within 24 hours to DWQ representatives or other oversight inspectors, e.g., U.S. Environmental Protection Agency [EPA] or a local MS4, on request, or immediately during an inspection on the site when there are workers and activity at the site.

- 4.2.12. Required Modifications of the SWPPP. The SWPPP must be modified as follows:
 - 4.2.12.a. During inspections when it is determined from observations of site conditions that storm water control measures are:
 - 4.2.12.a.i. Not adequate or not shown in the SWPPP, or
 - 4.2.12.a.ii. Changes in the SWPPP are necessary for compliance with this permit.
 - 4.2.12.b. When an oversight authority determines that the SWPPP is not adequate based on missing a required SWPPP or permit item, not addressing pollutants properly, not being up to date and reflecting current site conditions, or not being clear, thorough, and understandable.
- 4.2.13. SWPPP Modifications Deadline. Modifications to the SWPPP from inspections or oversight authority direction must occur before or during the next weekly inspection.

5. STANDARD PERMIT CONDITIONS.

5.1. Duty to Comply.

- 5.1.1. The permittee must comply with all conditions of this permit. Any permit noncompliance constitutes a violation of the Utah Water Quality Act (the Act) and is grounds for enforcement action; for permit termination, revocation and reissuance, or modification; or for denial of a permit renewal application.
- 5.1.2. Penalties for Violations of Permit Conditions
 - 5.1.2.a. *Violations*. The Act provides that any person who violates the Act, Utah wastewater or storm water rules, or conditions of a permit issued under the Act, is subject to a fine of \$10,000 per day.
 - 5.1.2.b. Willful or Gross Negligence. The Act provides that any person who discharges a pollutant to waters of the State as a result of criminal negligence or who intentionally discharges is criminally liable and is subject to imprisonment and a fine of up to \$50,000 per day (Utah Code Annotated 19-5-115).
 - 5.1.2.c. False Statements. The Act provides that any person who knowingly makes any false material statement, representation, or certification in any application, record, report, plan, or other document filed or required to be maintained under the Act, the rules, or this permit, or who knowingly falsifies, tampers with, or renders inaccurate, any monitoring device or method required to be maintained under the Act shall upon conviction, be punished by a fine of not more than \$10,000 or by imprisonment for 6 months, or by both (Utah Code Annotated 19-5-115(4)).
- 5.2. <u>Duty to Reapply</u>. If a permittee wishes to continue an activity regulated by this permit after the expiration date of this permit, the permittee must apply for and obtain a new permit except as provided in 1.6 and 1.7 of this permit.
- 5.3. Need to Halt or Reduce Activity not a Defense. It shall not be a defense for a permittee in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of this permit.
- 5.4. <u>Duty to Mitigate</u>. The permittee shall take all reasonable steps to minimize or prevent any discharge in violation of this permit that has a reasonable likelihood of adversely affecting human health or the environment.
- 5.5. <u>Duty to Provide Information</u>. The permittee shall furnish to the Director or an authorized representative, within a reasonable time, any information that is requested to determine compliance with this permit. The permittee must also furnish to the Director or an authorized representative copies of records to be kept by this permit.
- 5.6. Other Information. When the permittee becomes aware that he or she failed to submit any relevant facts or submitted incorrect information in the NOI or in any other report to the Director, he or she shall promptly submit such facts or information.

- 5.7. Oil and Hazardous Substance Liability. Nothing in this permit shall be construed to preclude the institution of any legal action or relieve the permittee from any responsibilities, liabilities, or penalties to which the permittee is or may be subject under the Act.
- 5.8. <u>Property Rights</u>. The issuance of this permit does not convey any property rights of any sort, nor any exclusive privileges, nor does it authorize any injury to private property nor any invasion of personal rights, nor any infringement of Federal, State or local laws or regulations.
- 5.9. Severability. The provisions of this permit are severable, and if any provision of this permit, or the application of any provision of this permit to any circumstance, is held invalid, the application of such provision to other circumstances, and the remainder of this permit shall not be affected thereby.
- 5.10. Record Retention. The permittee shall retain copies of SWPPPs and all reports required by this permit, and records of all data used to complete the NOI to be covered by this permit, for a period of at least three years from the date that the permit for the site is terminated (see 3.7). This period may be extended by request of the Director at any time.
- 5.11. <u>Addresses</u>. All written correspondence under this permit shall be directed to the DWQ at the following address:

Department of Environmental Quality Division of Water Quality 195 North 1950 West P.O. Box 144870 Salt Lake City, Utah 84114-4870

- 5.12. <u>State Laws</u>. Nothing in this permit shall be construed to preclude the institution of any legal action or relieve the permittee from any responsibilities, liabilities, or penalties established pursuant to any applicable State law or regulation under authority preserved by Utah Code Annotated 19-5-117.
 - 5.12.1. No condition of this permit shall release the permittee from any responsibility or requirements under other environmental statutes or regulations.
- 5.13. Proper Operation and Maintenance. The permittee shall at all times properly operate and maintain all facilities and systems of treatment and control and related appurtenances which are installed or used by the permittee to achieve compliance with the conditions of this permit and with the requirements of SWPPPs. Proper operation and maintenance also includes adequate laboratory controls and appropriate quality assurance procedures. Proper operation and maintenance requires the operation of backup or auxiliary facilities or similar systems, installed by a permittee only when necessary to achieve compliance with the condition of the permit.
- 5.14. <u>Inspection and Entry</u>. The permittee shall allow, upon presentation of credentials, the Director or an authorized representative to:
 - 5.14.1. Enter upon the permittee's premises where a regulated facility or activity is located or conducted or where records must be kept under the conditions of this permit;

- 5.14.2. Have access to and copy at reasonable times, any records that must be kept under the conditions of this permit.
- 5.14.3. Inspect at reasonable times any facilities, equipment (including monitoring and control equipment), practices or operations regulated or required under this permit; and
- 5.14.4. Sample or monitor at reasonable times for the purposes of assuring permit compliance or as otherwise authorized by law, any substances or parameters at any location.

5.15. Reopener Clause.

- 5.15.1. Reopener Due to Water Quality Impacts. If there is evidence indicating that the storm water discharges authorized by this permit cause, have the reasonable potential to cause, or contribute to a violation of a water-quality standard, the discharger may be required to obtain an individual permit or an alternative general permit in accordance with 1.7.4 of this permit or the permit may be modified to include different limitations and/or requirements.
- 5.15.2. *Reopener Guidelines*. Permit modification or revocation will be conducted according to Utah Administrative Code R317-8-5.6 and UAC R317-8-6.2.
- 5.15.3. Permit Actions. This permit may be modified, revoked and reissued, or terminated for cause. The filing of a request by the permittee for a permit modification revocation and reissuance, termination, a modification of planned changes or anticipated noncompliance does not stay any permit condition.

5.16. Signatory Requirements.

- 5.16.1. All NOIs, SWPPPs, reports, certifications or information submitted to the Director, or that this permit requires be maintained by the permittee, shall be signed as follows:
 - 5.16.1.a. All NOIs and SWPPPs shall be signed by both the owner or lessee of the project/property and the general contractor.
 - 5.16.1.b. All reports required by the permit and other information requested by the Director or by an authorized representative of the Director shall be signed by a person described above or by a duly authorized representative of that person. A person is a duly authorized representative only if:
 - 5.16.1.b.i. The authorization is made in writing by a person described above and submitted to the Director; and
 - 5.16.1.b.ii. The authorization specifies either an individual or a position having such as the position of manager, operator, superintendent, or position of equivalent responsibility or an individual or position having overall responsibility for environmental matters for the company. A duly authorized representative may therefore be either a named individual or any individual occupying a named position.
 - 5.16.1.c. *Certification*. Any person signing documents under 5.16 shall make the following certification:

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information including the possibility of fine and imprisonment for knowing violations.

5.16.2. If a document is to be signed electronically, the Division's rules regarding electronic transactions govern, if applicable.

6. DEFINITIONS

Arid Areas: Areas with an average annual rainfall of 10 inches or less.

Common Plan of Development (or sale): A plan to subdivide a parcel of land into separate parts for separate sale. This can be for a residential, commercial, or industrial development. The plan originates as a single parcel that is separated into parts. This usually goes through an approval process by a local governmental unit, but in some cases, it may not require that process. The original plan is considered the "common plan of development or sale" whether phased or completed in steps.

Additional information related to Common Plan of Development for Permit Purposes:

For UPDES storm water permit purposes, a common plan must have been initiated after October, 1992. A common plan of development or sale remains so until each lot or section of the development has fulfilled its planned purposes (e.g. in a residential development as homes are completed, stabilized, and sold or occupied). As lots or separated sections of the development are completed, the lot or section is stabilized, and the plan purposes are fulfilled for that area, lot, or section, it is no longer part of the common plan of development or sale (e.g. if a home is sold in a development and the owner decides to add a garage somewhere on the lot, that garage project is not part of the common plan of development or sale.

In this process a common plan of development or sale may become reduced in size and/or separated by completed areas which are no longer part of the common plan of development or sale, but all unfinished lots remain part of the same common plan development or sale until they are completed, stabilized, and fulfilled according to the purposes of the plan.

Construction Activity: Earth-disturbing activities, such as the clearing, grading, and excavation of land.

Construction Waste: Discarded material such as packaging materials, scrap construction materials, masonry products, timber, steel, pipe, and electrical cuttings, plastics, and Styrofoam.

Corrective Action: For the purposes of the permit, any action taken to 1) repair, modify, or replace any storm water control used at the site; 2) clean up and dispose of spills, releases, or other deposits found on the site; and 3) remedy a permit violation.

Dewatering: The act of draining rainwater and/or groundwater from building foundations, vaults, and trenches (Note: if dewatering is occurring on a construction site and it causes a discharge to waters of the State, it must be permitted separately under the General Permit for Construction Dewatering and Hydrostatic Testing, UPDES Permit UTG070000).

Director: The director of the Division of Water Quality.

Discharge Point: For the purposes of this permit, the location where collected and concentrated storm water flows are discharged from the construction site.

Final Stabilization: All disturbed areas must be covered by permanent structures such as pavement, concrete slab, building, etc., or for areas not covered by permanent structures but that are receiving 20 inches or more of average annual precipitation, vegetation has been established with a uniform (e.g.,

evenly distributed, without large bare areas) perennial vegetative cover equivalent to 70 percent of the natural background vegetative cover. In the case of areas that are not covered by permanent structures, but that are receiving less than 20 inches of average annual precipitation (arid areas, 0-10 inches; semi-arid areas, 10-20 inches), final stabilization is equivalent to the requirements of 2.6.3 of this permit, including the provisions for permanent stabilization.

Impervious Surface: For the purpose of this permit, any land surface with a low or no capacity for water infiltration including, but not limited to, pavement, sidewalks, parking areas, driveways, or rooftops.

Indian Country: Defined at 40 CFR §122.2 as follows:

- 1. All land within the limits of any Indian reservation under the jurisdiction of the United States Government, notwithstanding the issuance of any patent, and, including rights-of-way running through the reservation;
- 2. All dependent Indian communities within the borders of the United States whether within the originally or subsequently acquired territory thereof; and
- 3. All Indian allotments, the Indian titles to which have not been extinguished, including rights-of-ways running through the same.

Infeasible: Infeasible means not technologically possible or not economically practicable and achievable in light of best industry practices. DWQ notes that it is not intentional for permit storm water control efforts required in the permit to conflict with State water rights law. In the case of conflict, State water rights law supersedes.

Install or Installation: When used in connection with storm water controls, to connect or set in position storm water controls to make them operational.

Municipal Separate Storm Sewer System or MS4: A storm-sewer system owned and operated by a state, city, town, county, district, association, or other public body created by or pursuant to State law having jurisdiction over disposal of storm water that discharges to waters of the State (e.g., Sandy City owns and operates the MS4 within the jurisdiction of Sandy City, or essentially Sandy City is the MS4).

Natural Buffer: For the purposes of this permit, an area of undisturbed natural cover surrounding surface waters within which construction activities are restricted. Natural cover includes the vegetation, exposed rock, or barren ground that exists before earth-disturbing activities begin.

Oversight Authority: Oversight authorities for storm water permits are agents from the EPA, DWQ or the Municipality of jurisdiction, when they are addressing compliance of storm water permits.

Owner: For the purpose of this permit an owner has ownership of a property on which construction activity is taking place, but it also includes ownership of a project for which construction activity is occurring on property that is leased. An owner is the party that has ultimate control over construction plans and specifications, including the ability at the highest level to make modifications to those plans and specifications. "Owner" in this context is the party that has ultimate control over the destiny of a project.

Permittee: The owner and/or the general contractor (those that signed on the NOI), for the project.

Pollutant-Generating Activities: At construction sites, for the purposes of this permit, those activities that lead to or could lead to the generation of pollutants, either as a result of earth-disturbance or a related support activity. Some of the types of pollutants that are typically found at construction sites are as follows:

- Sediment
- Nutrients
- · Heavy metals
- · Pesticides and herbicides
- · Oil and grease
- · Bacteria and viruses
- · Trash, debris, and solids
- · Treatment polymers
- · Any other toxic chemicals

Pollution Prevention Measures: Storm water controls designed to reduce or eliminate the addition of pollutants to construction site discharges through analysis of pollutant sources, implementation of proper handling/disposal practices, employee education, and other actions.

Project Site: A project site is not necessarily contained within the property boundaries designated for the final construction objective, or property owned by the owner of the project. The project site includes all areas affected by the construction process where disturbances, storage, or other construction activity occurs. If an area outside of property boundaries is used for the construction process, DWQ assumes the permittee has the right to access and use that area and the permittee must also meet permit requirements in that area.

Receiving Water: A "Water(s) of the State" is as defined in UAC R317-1-1, into which the regulated storm water discharges (see waters of the State listed below).

Rumble Strip: A rigid ramp/track (often made of steel) that vehicles drive over that causes tires to flex and shake for the removal of dirt.

Semi-Arid Areas: Areas with an average annual rainfall of between 10 and 20 inches.

Stabilization: The use of vegetative and/or non-vegetative cover to prevent erosion and sediment loss in areas of disturbed soil exposed from the construction process.

Storm water: Means storm water runoff, snowmelt runoff, and surface runoff and drainage.

Storm Water Control Measures: Refers to any storm water control, BMP, or other method used to prevent or reduce the discharge of pollutants to waters of the state.

Storm Water Inlet: An entrance or opening to a storm water conveyance system, generally placed below grade so as to receive storm water drainage from the surrounding area.

Storm Event: A precipitation event that results in a measurable amount of precipitation.

Track Out Pad: A track out pad is a pad normally made up of 4 to 6 inches of up to 6 inch cobble rocks or gravel of various size (the size is sometimes specified by a local MS4). Sometimes it is underlain with a fabric to keep dirt and mud separated from rock or gravel. It is wide enough to underlay the tires of any/all traffic leaving a construction site as vehicles exit the site. Its function is to flex and shake the tires to dislodge mud and dirt from the tires of vehicles leaving the construction site. Track out pads must be stirred or worked periodically so that mud or dirt collected is moved to the bottom and the rock/gravel on the pad is clean and effective dislodging more mud/dirt.

Waters of the State: All streams, lakes, ponds, marshes, watercourses, waterways, wells, springs, irrigation systems, drainage systems, and all other bodies or accumulations of water, surface and underground, natural or artificial, public or private, that are contained within, flow through, or border upon this state or any portion thereof, except that bodies of water confined to and retained within the limits of private property, and that do not develop into or constitute a nuisance, or a public health hazard, or a menace to fish and wildlife, shall not be considered to be "Waters of the State" under this definition (see Utah Code Annotated, 19-5-102(23)(a) &(b), and UAC R317-1-1).

APPENDIX E: Inspection Reports

INSPECTION REPORT INSPECTION PERIOD: 2012.03.01-2012.03.07 INSPECTOR: jd				SITE NAME: John Doe Project LAST RAIN EVENT: 2012.03.01 CURRENT WEATHER: clear							
							ВМР	DATE	OK/NOT OK?	BMP CONDITION	CORRECTIVE ACTION REQUIREMENTS
							Are all pollution sources controlled? Do any other problems exist?	3/7/2012	ОК	na	All pollution sources are controlled. No new BMPs are necessary.
4.7.2 LOT Cutdown	3/7/2012	OK	In place								
4.7.1 Silt Fencing	3/7/2012	Empresant and a second and a se	Silt fence at south boundary was buried by excavator.	Informed syz excating by phone this must be repaired including the sediment washed onto the adjacent lot, no later than two days or before the next storm event which ever comes first. Sediment had washed onto the south property							
4.9.1 Drop Inlet Bags	3/7/2012	OK	Only about 4" of sediment	The second of th							
4.9.2 Gutter Dans	3/7/2017	OK	Gutter dams are tight to the curb and free of sediment	Gutter dams were clean March 3rd in anticipation of the forecast storm on March 4th. The dams were also cleaned on the 5th following the storm.							
4.10.1 Dust Controls	3/7/2012	ОК	Water and hose are ready. No wind today.	Wind did blow the morning of March 3rd before the storm. City warned my excavator. The excavator began watering as he was loading.							
5.1,2 Grave! Parking	3/7/2012	na	not scheduled per SWPPP	The grave-pad area is covered with excavation from the footing and foundation.							
5.1.3 Tpost and Tape	3/7/2012	OK	fence post and tape in place.	Excavation ceased during the March 4th storm. Excavator needed to access at a point not shown on SWPPP. Ground was dry and barrier tape was but back.							
5.1.4 Sq Nose Shovel and Broom	3/7/2012	ОК	Minor tracking today	Minor tracking occurred on March 6th. The excavator's laborer cleaned the road with a hand broom and shovel in the middle of the day and at the end.							
5.2.1 Dumpster	3/7/2012	na	not scheduled per SWPPP	Subs have been told to carry out any lunch trash.							
5.2.3 Portable Toilet	3/7/2012	OK	In place.								
5.2.5 Concrete Washout	3/7/2012	OK	In place. About 25% full.								
5.3.2 Material Storage	3/7/2012	OK	No materials being stored								
5.3.3 Construction Staging	3/7/2012		not scheduled per SWPPP								
5.3.4 Spoil Waste Limits	3/7/2012	not OK	see 2.5	see 2.5							
5.5 Sp.1 Kg	3/7/2012	OK	In place								
o.8,1 Frontage Swale	3/7/2012		not scheduled per SWPPP								

Lectify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Name: 10111 Do. Co Title: Counciv Date: 2012-03-07

APPENDIX F: Corrective Action Log

Corrective Action Log							
Date & Time of Inspection/ Random Notice of Problem	Inspectio n or Randomly Noticed?	BMP # and Name	Description of BMP Deficiency (or reference the inspection report)	Init ial	Correction Date (MM/DD/ YY)	How the BMP was Corrected	SWPP P Chan ged (Y/N)
-							
					na municipal programa de la companya del companya del companya de la companya de		Table and the second se
					ngla sayah daganan Ag		
					The second secon		
			25				
					The second secon	A management of the state of th	
					The second secon		

APPENDIX G: Amendment Log

		Amendment	Log		
Amendme nt No.	Description of the Amendment	Date of Amendment	Amendment Prepared by [Name(s) and Title]		
-					
			8		
The state of the s					

APPENDIX H: Certifications,	Agreements, and Delega	tion of Authority	

APPENDIX I: Grading and Stabilization Activities Log

Project Name: Click here to enter text.


SWPPP Contact: Click here to enter text.

Date Grading Activity Initiated	Description of Grading Activity	Date Grading Activity Ceased (Indicate Temporary or Permanent)	Date When Stabilization Measures are Initiated	Description of Stabilization Measure and Location
	Name Annual Annu			

APPENDIX J: Construction Plans

APPENDIX K: Additional Information (i.e. permits such as local permits, dewatering, stream alteration, wetland, and out of date SWPPP documents, etc.)

APPENDIX L: BMP Specifications and Details (label BMPs to match the sections identified in this document.)



A temporary sediment barrier consisting of entrenched filter fabric stretched across and secured to supporting posts.

APPLICATION:

- Perimeter control: place barrier at downgradient limits of disturbance
- Sediment barrier: place barrier at toe of slope or soil stockpile
- Protection of existing waterways: place barrier at top of stream bank
- Inlet protection: place fence surrounding catchbasins

INSTALLATION/APPLICATION CRITERIA:

- Place posts 6 feet apart on center along contour (or use preassembled unit) and drive 2 feet minimum into ground. Excavate an anchor trench immediately upgradient of posts.
- Secure wire mesh (14 gage min. With 6 inch openings) to upslope side of posts. Attach with heavy duty 1 inch long wire staples, tie wires or hog rings.
- Cut fabric to required width, unroll along length of barrier and drape over barrier. Secure fabric to mesh with twine, staples, or similar, with trailing edge extending into anchor trench.
- Backfill trench over filter fabric to anchor.

LIMITATIONS:


- Recommended maximum drainage area of 0.5 acre per 100 feet of fence
- Recommended maximum upgradient slope length of 150 feet
- ► Recommended maximum uphill grade of 2:1 (50%)
- ► Recommended maximum flow rate of 0.5 cfs
- Ponding should not be allowed behind fence

MAINTENANCE:

- Inspect immediately after any rainfall and at least daily during prolonged rainfall.
- Look for runoff bypassing ends of barriers or undercutting barriers.
- Repair or replace damaged areas of the barrier and remove accumulated sediment.
- Reanchor fence as necessary to prevent shortcutting.
- Remove accumulated sediment when it reaches ½ the height of the fence.

OBJECTIVES

- Housekeeping Practices
- Contain Waste
- ☐ Minimize Disturbed Areas
- ☐ Stabilize Disturbed Areas
- ☑ Protect Slopes/Channels
- ☑ Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- □ Nutrients
- □ Toxic Materials
- ☐ Oil & Grease
- ☐ Floatable Materials
- □ Other Waste
- High Impact
- Medium Impact
- ☐ Low or Unknown Impact

- Capital Costs
- O&M Costs
- Maintenance
- ☐ Training
- High
- Medium
- □ Low

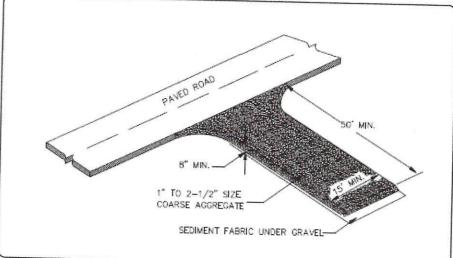

A stabilized pad of crushed stone located where construction traffic enters or leaves the site from or to paved surface.

APPLICATIONS:

At any point of ingress or egress at a construction site where adjacent traveled way is paved. Generally applies to sites over 2 acres unless special conditions exist.

INSTALLATION/APPLICATION CRITERIA:

- Clear and grub area and grade to provide maximum slope of 2%.
- Compact subgrade and place filter fabric if desired (recommended for entrances to remain for more than 3 months.
- Place coarse aggregate, 1 to 2-1/2 inches in size, to a minimum depth of 8 inches.

LIMITATIONS:

- Requires periodic top dressing with additional stones.
- Should be used in conjunction with street sweeping on adjacent public rightof-way.

MAINTENANCE:

- Inspect daily for loss of gravel or sediment buildup.
- Inspect adjacent roadway for sediment deposit and clean by sweeping or shoveling.
- Repair entrance and replace gravel as required to maintain control in good working condition.
- Expand stabilized area as required to accommodate traffic and prevent erosion at driveways.

OBJECTIVES

- Housekeeping Practices
- ☐ Contain Waste
- ☐ Minimize Disturbed Areas
- ☐ Stabilize Disturbed Areas
- ☐ Protect Slopes/Channels
- Control Site PerimeterControl Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- □ Nutrients
- □ Toxic Materials
- □ Oil & Grease
- ☐ Floatable Materials
- ☐ Other Waste
- High Impact
- Medium Impact
- □ Low or Unknown Impact

- Capital Costs
- O&M Costs
- Maintenance
- □ Training
- High
- Medium
- □ Low



Prevent or reduce the discharge of pollutants to storm water from concrete waste by conducting washout off-site, performing on-site washout in a designated area, and training employees and subcontractors.

APPLICATIONS:

This technique is applicable to all types of sites.

INSTALLATION/APPLICATION CRITERIA:

- Store dry and wet materials under cover, away from drainage areas.
- Avoid mixing excess amounts of fresh concrete or cement on-site.
- Perform washout of concrete trucks off-site or in designated areas only.
- Do not wash out concrete trucks into storm drains, open ditches, streets, or
- Do not allow excess concrete to be dumped on-site, except in designated areas.
- When washing concrete to remove fine particles and expose the aggregate, avoid creating runoff by draining the water within a bermed or level area. (See Earth Berm Barrier information sheet.)
- Train employees and subcontractors in proper concrete waste management.

LIMITATIONS:


Off-site washout of concrete wastes may not always be possible.

MAINTENANCE:

- Inspect subcontractors to ensure that concrete wastes are being properly managed.
- If using a temporary pit, dispose hardened concrete on a regular basis.

OBJECTIVES

- Housekeeping Practices
- Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- Protect Slopes/Channels Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- П **Nutrients**
- П Toxic Materials
- Oil & Grease
- Floatable Materials
- Other Construction Waste
- High Impact
- X Medium Impact
- Low or Unknown Impact

- Capital Costs П
- O&M Costs
- X Maintenance
- x Training
- High
- X Medium
- I OW

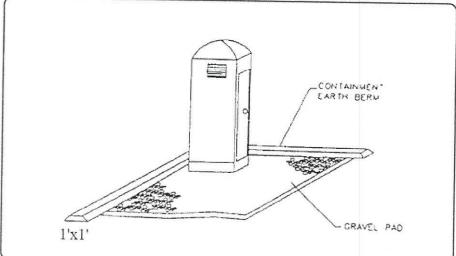

Temporary on-site sanitary facilities for construction personnel.

APPLICATION:

All sites with no permanent sanitary facilities or where permanent facility is too far from activities.

INSTALLATION/APPLICATION CRITERIA:

- Locate portable toilets in convenient locations throughout the site.
- Prepare level, gravel surface and provide clear access to the toilets for servicing and for on-site personnel.
- Construct earth berm perimeter (See Earth Berm Barrier Information Sheet), control for spill/protection leak.

LIMITATIONS:

No limitations.

MAINTENANCE:

- ▶ Portable toilets should be maintained in good working order by licensed service with daily observation for leak detection.
- Regular waste collection should be arranged with licensed service.
- All waste should be deposited in sanitary sewer system for treatment with appropriate agency approval.

OBJECTIVES

- × Housekeeping Practices
- × Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- Protect Slopes/Channels Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- Nutrients
- Toxic Materials
- Oil & Grease
- П Floatable Materials
- Other Construction Waste
- High Impact
- × Medium Impact
- Low or Unknown Impact

- × Capital Costs
- × O&M Costs
- × Maintenance
- Training
- High
- × Medium
- Low

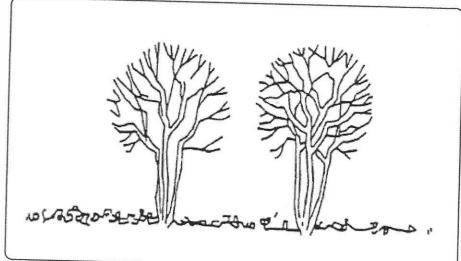

Carefully planned preservation of existing vegetation minimizes the potential of removing or injuring existing trees, vines, shrubs and/or grasses that serve as erosion controls.

APPLICATIONS:

This technique is applicable to all types of sites. Areas where preserving vegetation can be particularly beneficial are floodplains, wetlands, stream banks, steep slopes, and other areas where erosion controls would be difficult to establish, install, or maintain.

INSTALLATION/APPLICATION CRITERIA:

- Clearly mark, flag or fence vegetation or areas where vegetation should be preserved.
- Prepare landscaping plans which include as much existing vegetation as possible and state proper care during and after construction.
- Define and protect with berms, fencing, signs, etc. a setback area from vegetation to be preserved.
- Propose landscaping plans which do not include plant species that compete with the existing vegetation.
- Do not locate construction traffic routes, spoil piles, etc. where significant adverse impact on existing vegetation may occur.

LIMITATIONS:


- Requires forward planning by the owner/developer, contractor and design
- For sites with diverse topography, it is often difficult and expensive to save existing trees while grading the site satisfactorily for the planned development.
- May not be cost effective with high land costs.

MAINTENANCE:

- Inspection and maintenance requirements for protection of vegetation are
- Maintenance of native trees or vegetation should conform to landscape plan specifications.

OBJECTIVES

- Housekeeping Practices П
 - Contain Waste
- Minimize Disturbed Areas ×
- X Stabilize Disturbed Areas
- × Protect Slopes/Channels
- × Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- Nutrients
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- Medium Impact X
- Low or Unknown Impact

- Capital Costs
- O&M Costs
- Maintenance
- Training
- High
- X Medium
- Low



Prevent or reduce the discharge of pollutants to stormwater from building repair, remodeling and construction by using soil erosion controls, enclosing or covering building material storage areas, using good housekeeping practices, using safer alternative products, and training employees.

APPROACH:

- Use soil erosion control techniques if bare ground is temporarily exposed.
- Use permanent soil erosion control techniques if the remodeling clears buildings that are not to be replaced.
- Enclose painting operations consistent with local air quality regulations and OSHA.
- Properly store materials that are normally used in repair and remodeling such as paints and solvents.
- Properly store and dispose waste materials generated from the activity.
- Maintain good housekeeping practices while work is underway.

LIMITATIONS:

- ► This BMP is for minor construction only.
- Hazardous waste that cannot be re-used or recycled must be disposed of by a licensed hazardous waste hauler.
- Safer alternative products may not be available, suitable, or effective in every case.
- Be certain that actions to help stormwater quality are consistent with OSHA and air quality regulations.

OBJECTIVES

- □ New Development
- ☐ Residential
- Commercial Activities
- Industrial Activities
- Municipal Facilities
- ☐ Illegal Discharges




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- ☐ Nutrients
- Heavy Metals
- ▼ Toxic Materials
- ☐ Oxygen Demanding Substance
- ☑ Oil & Grease
- Floatable Materials
- □ Bacteria & Viruses
- High Impact
- Medium Impact
- ☐ Low or Unknown Impact

- Capital Costs
- ☑ O&M Costs
- □ Regulatory
- ☑ Training
- Staffing
- Administrative
- High
- Medium
- □ Low

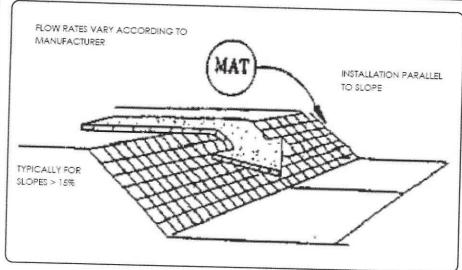

Mats made of natural or synthetic material, which are used to temporarily or permanently stabilize soil.

APPLICATION:

- Typically suited for post-construction site stabilization, but may be used for temporary stabilization of highly erosive soils.
- Channels and streams.
- Steep slopes.

INSTALLATION/APPLICATION CRITERIA:

- ▶ Mats may be applied to disturbed soils and where existing vegetation has
- The following organic matting materials provide temporary protection until permanent vegetation is established, or when seasonal circumstances dictate the need for temporary stabilization until weather or construction delays are resolved: Jute mats and straw mats.
- The following synthetic mats may be used for either temporary or postconstruction stabilization, both with and without vegetation: excelsior matting, glass fiber matting, and mulch matting.
- Staples are needed to anchor the matting.

LIMITATIONS:

- Mats are more costly than other BMP practices, limiting their use to areas where other BMPs are ineffective (e.g., channels, steep slopes). May delay seed germination, due to reduction in soil temperature.
- Installation requires experienced contractor to ensure soil stabilization and erosion protection.

MAINTENANCE:

- Inspect monthly and after significant rainfall.
- Re-anchor loosened matting and replace missing matting and staples as

OBJECTIVES

- Housekeeping Practices
- П Contain Waste
- Minimize Disturbed Areas
- × Stabilize Disturbed Areas
- X Protect Slopes/Channels П
- Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- X Medium Impact
- Low or Unknown Impact

- Capital Costs
- × O&M Costs
- × Maintenance
- Training
- High
- X Medium
- Low

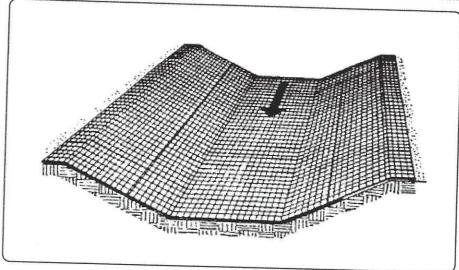

Erosion control blankets are used in place of mulch on areas of high velocity runoff and/or steep grade, to aid in controlling erosion on critical areas by protecting young vegetation.

APPLICATIONS:

- Where vegetation is likely to grow too slowly to provide adequate cover.
- In areas subject to high winds where mulch would not be effective.

INSTALLATION/APPLICATION CRITERIA:

- Install erosion control blankets parallel to the direction of the slope.
- In ditches, apply in direction of the flow.
- Place erosion control blankets loosely on soil do not stretch.
- Ends of blankets should be buried no less than six inches deep.
- Staple the edges of the blanket at least every three feet.

LIMITATIONS:

Not recommended in areas which are still under construction.

MAINTENANCE:

- Check for erosion and undermining periodically, particularly after rainstorms.
- Repair dislocations or failures immediately.
- If washouts occur, reinstall after repairing slope damage.
- Monitor until permanently stabilized.

OBJECTIVES

- Housekeeping Practices
 - Contain Waste
- П Minimize Disturbed Areas
- × Stabilize Disturbed Areas ×
- Protect Slopes/Channels Control Site Perimeter П
- Control Internal Erosion



ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- x **Nutrients**
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- X Medium Impact
- Low or Unknown Impact

- Capital Costs
- × O&M Costs
- X Maintenance
 - Training
- High
- X Medium
- П Low



OBJECTIVES

- Housekeeping Practices
- × Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- Protect Slopes/Channels
- Control Site Perimeter
- Control Internal Erosion

DESCRIPTION: Practices to clean-up leakage/spillage of on-site materials that may be harmful to

APPLICATION:

All sites

receiving waters.

GENERAL:

- Store controlled materials within a storage area.
- Educate personnel on prevention and clean-up techniques.
- Designate an Emergency Coordinator responsible for employing preventative practices and for providing spill response.
- Maintain a supply of clean-up equipment on-site and post a list of local response agencies with phone numbers.

METHODS:

- Clean-up spills/leaks immediately and remediate cause.
- Use as little water as possible. NEVER HOSE DOWN OR BURY SPILL CONTAMINATED MATERIAL.
- Use rags or absorbent material for clean-up. Excavate contaminated soils. Dispose of clean-up material and soil as hazardous waste.
- Document all spills with date, location, substance, volume, actions taken and other pertinent data.
- Contact local Fire Department and State Division of Environmental Response and Remediation (Phone #536-4100) for any spill of reportable quantity.

EBER COL


ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- Toxic Materials
- X Oil & Grease
- Floatable Materials
- Other Construction Waste
- High Impact
- X Medium Impact
- Low or Unknown Impact

- X Capital Costs
- O&M Costs
- Maintenance
- Training
- High
- X Medium
- Low

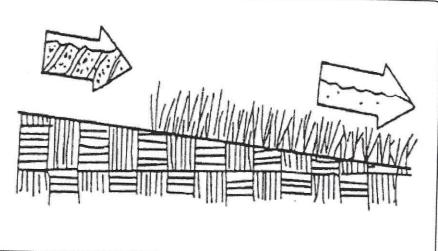

Seeding of grass and plantings of trees, shrubs, vines and ground covers provide long-term stabilization of soil. In some areas, with suitable climates, grasses can be planted for temporary stabilization.

APPLICATION:

- Appropriate for site stabilization both during and after construction
- Any graded/cleared areas where construction activities have ceased.
- Open space cut and fill areas.
- Steep slopes, spoil piles, vegetated swales, landscape corridors, stream

INSTALLATION/APPLICATION CRITERIA:

Type of vegetation, site and seedbed preparation, planting time, fertilization and water requirements should be considered for each application. Grasses:

- Ground preparation: fertilize and mechanically stabilize the soil.
- Tolerant of short-term temperature extremes and waterlogged soil composition
- Appropriate soil conditions: shallow soil base, good drainage, slope 2:1 or flatter.
- Mowing, irrigating, and fertilizing are vital for promoting vigorous grass growth.

Trees and Shrubs:

- Selection criteria: vigor, species, size, shape & wildlife food source.
- Soil conditions: select species appropriate for soil, drainage & acidity.
- Other factors: wind/exposure, temperature extremes, and irrigation needs. Vines and Ground Covers:
- Ground preparation: lime and fertilizer preparation.
- Use proper seeding rates.
- Appropriate soil conditions: drainage, acidity and slopes.
- Generally avoid species requiring irrigation.

LIMITATIONS:

- Permanent and temporary vegetation may not be appropriate in dry periods
- Fertilizer requirements may have potential to create stormwater pollution.

MAINTENANCE:

- Shrubs and trees must be adequately watered and fertilized and if needed pruned.
- Grasses may need to be watered and mowed.

OBJECTIVES

- Housekeeping Practices
 - Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- X Protect Slopes/Channels
- Control Site Perimeter
- Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- × **Nutrients**
- × Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- 5 High Impact
- X Medium Impact
- П Low or Unknown Impact

- X Capital Costs
- X **O&M** Costs
- X Maintenance
- Training
- High
- X Medium
- Low



OBJECTIVES

- Housekeeping Practices
- Contain Waste
- Minimize Disturbed Areas
- П Stabilize Disturbed Areas
- × Protect Slopes/Channels
- Control Site Perimeter X
- Control Internal Erosion

DESCRIPTION:

Stacking sand bags along a level contour creates a barrier which detains sediment laden water, ponding water upstream of the barrier and promoting sedimentation.

APPLICATION:

- Along the perimeter of the site.
- May be used in drainage areas up to 5 acres.
- Along streams and channels
- Across swales with small catchments.
- Around temporary spoil areas.
- Below the toe of a cleared slope.

INSTALLATION/APPLICATION CRITERIA:

- Install along a level contour.
- Base of sand bag barrier should be at least 48 inches wide.
- Height of sand bag barrier should be at least 18 inches high.
- 4 inch PVC pipe may be installed between the top layers of sand bags to drain large flood flows.
- Provide area behind barrier for runoff to pond and sediment to settle.
- Place below the toe of a slope.

LIMITATIONS:

- Sand bags are more expensive than other barriers, but also more durable.
- Burlap should not be used.

MAINTENANCE:

- Inspect after each rain.
- Reshape or replace damaged sand bags immediately.
- Replace sediment when it reaches six inches in depth.


ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- X Medium Impact
- Low or Unknown Impact

- Capital Costs
- O&M Costs
- Maintenance
- Training
- High
- Medium
- Low

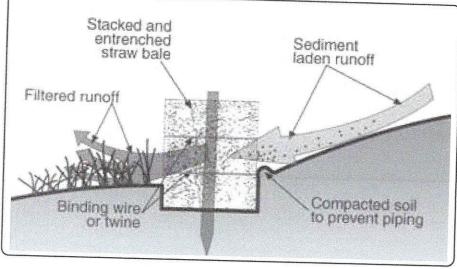

OBJECTIVES

- Housekeeping Practices
- Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- × Protect Slopes/Channels
- X Control Site Perimeter
- Control Internal Erosion

DESCRIPTION:

Temporary sediment barrier consisting of a row of entrenched and anchored straw bales.

APPLICATION:

- Perimeter Control: place barrier at downgradient limits of disturbance.
- Sediment barrier: place barrier at toe of slope or soil stockpile.
- Protection of existing waterways: place barrier at top of stream bank.
- Inlet Protection.

INSTALLATION/APPLICATION CRITERIA:

- Excavate a 4-inch minimum deep trench along contour line, i.e. parallel to slope, removing all grass and other material that may allow underflow.
- Place bales in trench with ends tightly abutting; fill any gaps by wedging loose straw into openings.
- Anchor each bale with 2 stakes driven flush with the top of the bale.
- Backfill around bale and compact to prevent piping, backfill on uphill side to be built up 4-inches above ground at the barrier.

LIMITATIONS:

- Recommended maximum area of 0.5 acre per 100 feet of barrier
- Recommended maximum upgradient slope length of 150 feet
- Recommended maximum uphill grade of 2:1 (50%)

MAINTENANCE:

- Inspect immediately after any rainfall and at least daily during prolonged
- Look for runoff bypassing ends of barriers or undercutting barriers.
- Repair or replace damaged areas of the barrier and remove accumulated
- Realign bales as necessary to provide continuous barrier and fill gaps.
- Recompact soil around barrier as necessary to prevent piping.


ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- Toxic Materials
- П Oil & Grease
- Floatable Materials
- Other Waste
- High Impact
- × Medium Impact
- Low or Unknown Impact

- X Capital Costs
- O&M Costs
- X Maintenance
- П Training
- High
- X Medium
- Low

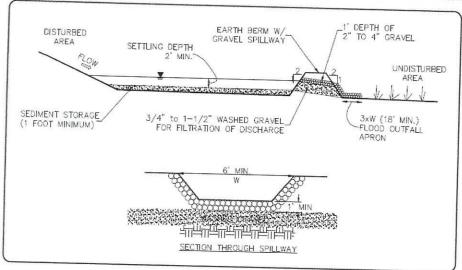

A sediment trap is a small excavated or bermed area where runoff from small drainage areas is detained and sediment can settle.

APPLICATION:

- Temporary control for runoff from disturbed areas of less than 3 acres.
- Temporary control for discharge from diversion dike, surface benching, or other temporary drainage measures.

INSTALLATION/APPLICATION CRITERIA:

- Design basin for site specific location.
- Excavate basin or construct compacted berm containment.
- Construct outfall spillway with apron.
- Provide downstream silt fence if necessary.

LIMITATIONS:


- Should be sized based on anticipated runoff, sediment loading and drainage
- May require silt fence at outlet for entrapment of very fine silts and clays.

MAINTENANCE:

- Inspect after each rainfall event and at a minimum of monthly.
- Repair any damage to berm, spillway or sidewalls.
- Remove accumulated sediment as it reaches 2/3 height of available
- Check outlet for sedimentation/erosion of downgradient area and remediate as necessary. Install silt fence if sedimentation apparent.

OBJECTIVES

- Housekeeping Practices
- Contain Waste
- Minimize Disturbed Areas
- Stabilize Disturbed Areas
- Protect Slopes/Channels Control Site Perimeter
- × Control Internal Erosion




ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- X Toxic Materials
- Oil & Grease
- П Floatable Materials
- П Other Waste
- High Impact
- × Medium Impact
- Low or Unknown Impact

- X Capital Costs
- X O&M Costs
- П Maintenance
- П Training
- High
- X Medium
- Low

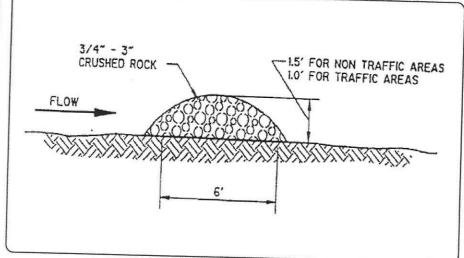

OBJECTIVES

- Housekeeping Practices
- П Contain Waste
- П Minimize Disturbed Areas
- П Stabilize Disturbed Areas X
- Protect Slopes/Channels ×
- Control Site Perimeter
- Control Internal Erosion

DESCRIPTION:

A rock filter is made of rock 3/4 - 3" in diameter and placed along a level contour. A brush filter is composed of brush (usually obtained during the site clearing) wrapped in filter cloth and anchored to the toe of the slope. If properly anchored brush or rock filters may be used for sediment trapping and velocity reduction.

APPLICATION:

- As check dams across mildly sloped construction roads.
- Below the toe of slopes.
- -Along the site perimeter.
- In areas where sheet or rill flow occurs.
- Around temporary spoil areas.
- At sediment traps or culvert/pipe outlets.

INSTALLATION/APPLICATION CRITERIA:

- For rock filter, use larger rock and place in staked, woven wire sheathing if placed where concentrated flows occur.
- Install along a level contour.
- Leave area behind berm where runoff can pond and sediment can settle.
- Drainage areas should not exceed 5 acres.

LIMITATIONS:

- Rock berms may be difficult to remove.
- Removal problems limit their usefulness in landscaped areas.
- Runoff will pond upstream of the filter, possibly causing flooding if sufficient space does not exist.

MAINTENANCE:

- Inspect monthly after each rainfall.
- If berm is damaged, reshape and replace lost/dislodged rock
- Remove sediment when depth reaches 1/3 of berm height, or 1 ft.


ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- **Nutrients**
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- X Medium Impact
- П Low or Unknown Impact

- Capital Costs
- X O&M Costs
- Maintenance
- Training
- High
- X Medium
- Low

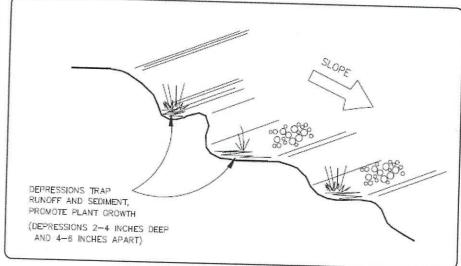

Rough preparation of working areas leaving depressions and uneven surface. Depressions should be done parallel to contours.

APPLICATION:

Surface roughening is appropriate for all construction that will not be receiving impervious cover within 14 days and that will be exposed less than 60 days (seed areas to be open in excess of 60 days).

INSTALLATION/APPLICATION CRITERIA:

- Surface should be left in rough condition during initial earthwork activity.
- Surfaces that have become smoothed or compacted due to equipment traffic should be roughened by use of disks, spring harrows, teeth on front end loader, or similar, operating along the contours of the slope. Tracking (by crawler tractor driving up and down slope) may also be used to provide depressions parallel to contours.
- Avoid compaction of soils during roughening as this inhibits plant growth and promotes storm water runoff. Limit tracked machinery to sandy soil.
- Seed or mulch areas to be exposed in excess of 60 days.
- Employ dust controls. (See Dust Control Detail Sheet).

LIMITATIONS:


- Will not withstand heavy rainfall.
- Slopes steeper than 2:1 (50%) should be benched. (See Benching Detail Sheet).

MAINTENANCE:

- Inspect following any storm event and at a minimum of weekly.
- If erosion in the form of rills (small waterways formed by runoff) is evident, perform machine roughening of area.
- For vegetated slopes reseed areas that are bare or have been reworked.

OBJECTIVES

- Housekeeping Practices П
 - Contain Waste
- Minimize Disturbed Areas
- X Stabilize Disturbed Areas
- × Protect Slopes/Channels Control Site Perimeter
- Control Internal Erosion



ENGINEERING DEPARTMENT

2380 Washington Blvd., Suite 240 Ogden, UT 84401 (801) 399-8374

TARGETED POLLUTANTS

- Sediment
- Nutrients
- Toxic Materials
- Oil & Grease
- Floatable Materials
 - Other Waste
- High Impact
- Medium Impact X
- Low or Unknown Impact

- Capital Costs
- × O&M Costs
- X Maintenance
- Training
- High
- × Medium
- П Low
