



Construction Observation Report # 1


Project	Uintah Bybee Water Tanks	Project Number	20218
Location	6393 Bybee Dr, Ogden, UT	Date & Time	02/24/2023 1:30PM
Civil Engineer	Jones and Associates	Weather	Clear
Contractor	FX Construction	Observer	Jami Havens


Persons Present: Pedro (FX Construction), Matt (Jones and associate), Zac (Jones and Associates)

Project Status Summary: Foundations have been placed. Reinforcement of the walls is complete. Wall forms are being placed.

Items of Note:				
Item No.:	Item:	Follow-Up / Action Required:	Initials	Photo:
1-1	The dowels between the top of the wall and the roof slab shown in detail 1 on sheet S3 have not been placed.	Ensure that dowels are installed with the compressible insulation prior to placement of wall concrete.		1

End of Report


 Prepared By:


 Reviewed By:

Corrective Action Summary			
Items above requiring corrective action must be satisfactorily completed prior to being inaccessible or being covered. The Project Superintendent and/or subcontractor responsible shall verify the work by initialing in the space above describing the action required. The project superintendent is requested to sign below upon completion and provide a copy via fax or e-mail to the Architect and Engineer.			
Superintendent Signature		Date	

Distribution
<input checked="" type="checkbox"/> Project File <input checked="" type="checkbox"/> Architect <input type="checkbox"/> Contractor <input type="checkbox"/> Other (list)

20218_cor01_20230224.docx

This Observation Report is the file record of the above noted site visit by ARW Engineers personnel. The Observation Visit was made in accordance with the ARW Engineers/Client agreement for services and/or governing building codes. Observation Visits are not intended to be comprehensive inspections. Observation visits and associated reports are not an approval or warranty of the contractors work nor is the Observation a Special Inspection. Means, methods and sequencing of construction as well as job site safety were not addressed or reviewed and are not the responsibility of ARW Engineers.

Photos



Photo 1



Construction Observation Report # 2


Project	Uintah Bybee Water Tanks	Project Number	20218
Location	6393 Bybee Dr, Ogden, UT	Date & Time	03/15/2023 1:30PM
Civil Engineer	Jones and Associates	Weather	Clear
Contractor	FX Construction	Observer	Jami Havens

Persons Present: Pedro (FX Construction)

Project Status Summary: Concrete walls have been placed. Reinforcement of the deck is about 75% complete.

Items of Note:				
Item No.:	Item:	Follow-Up / Action Required:	Initials	Photo:
1-1	The #7 bars in the top layer of the column strips are 1 foot short on each end.	Replace the rebar with the correct length or add additional an additional #7 bar spliced on to each #7 bar that is short. See detail 2/S1 for the required splice lengths.		1

End of Report


 Prepared By:

Corrective Action Summary			
Items above requiring corrective action must be satisfactorily completed prior to being inaccessible or being covered. The Project Superintendent and/or subcontractor responsible shall verify the work by initialing in the space above describing the action required. The project superintendent is requested to sign below upon completion and provide a copy via fax or e-mail to the Architect and Engineer.			
Superintendent Signature		Date	

Distribution
<input checked="" type="checkbox"/> Project File <input checked="" type="checkbox"/> Architect <input type="checkbox"/> Contractor <input type="checkbox"/> Other (list)

20218_cor02_20230315.docx

This Observation Report is the file record of the above noted site visit by ARW Engineers personnel. The Observation Visit was made in accordance with the ARW Engineers/Client agreement for services and/or governing building codes. Observation Visits are not intended to be comprehensive inspections. Observation visits and associated reports are not an approval or warrantee of the contractors work nor is the Observation a Special Inspection. Means, methods and sequencing of construction as well as job site safety were not addressed or reviewed and are not the responsibility of ARW Engineers.

Photos



Photo 1

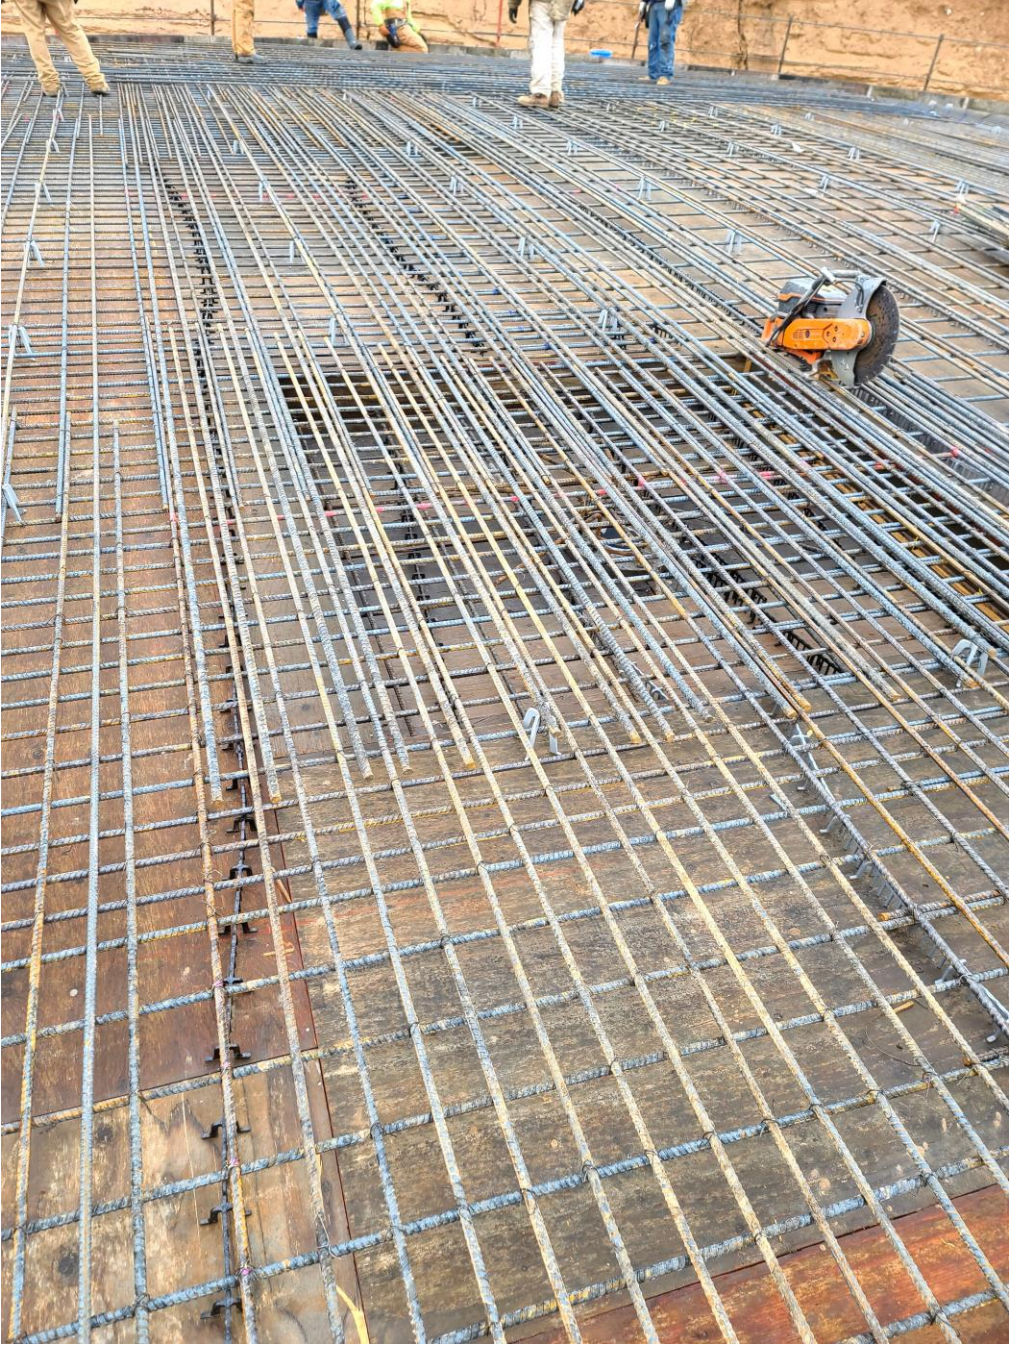


Photo 2



Construction Observation Report #3


Project	Uintah Bybee Water Tanks	Project Number	20218
Location	6393 Bybee Dr, Ogden, UT	Date & Time	07/19/2023 11:00AM
Civil Engineer	Jones and Associates	Weather	Clear
Contractor	FX Construction	Observer	Jami Havens

Persons Present: Pedro (FX Construction)

Project Status Summary: The first tank is completed and in service. The second tank footings have been placed. Reinforcement for the walls is approximately 75% complete.

Items of Note:				
Item No.:	Item:	Follow-Up / Action Required:	Initials	Photo:
1-1	No items of note were observed during this visit			1

End of Report


 Prepared By:

Corrective Action Summary			
Items above requiring corrective action must be satisfactorily completed prior to being inaccessible or being covered. The Project Superintendent and/or subcontractor responsible shall verify the work by initialing in the space above describing the action required. The project superintendent is requested to sign below upon completion and provide a copy via fax or e-mail to the Architect and Engineer.			
Superintendent Signature		Date	

Distribution
<input checked="" type="checkbox"/> Project File <input checked="" type="checkbox"/> Architect <input type="checkbox"/> Contractor <input type="checkbox"/> Other (list)

20218_cor03_20230719.docx

This Observation Report is the file record of the above noted site visit by ARW Engineers personnel. The Observation Visit was made in accordance with the ARW Engineers/Client agreement for services and/or governing building codes. Observation Visits are not intended to be comprehensive inspections. Observation visits and associated reports are not an approval or warrantee of the contractors work nor is the Observation a Special Inspection. Means, methods and sequencing of construction as well as job site safety were not addressed or reviewed and are not the responsibility of ARW Engineers.

Photos



Photo 1
