

Weber County Stormwater Construction Activity Permit

Application submittals will be accepted by appointment only. (801) 399-8374. 2380 Washington Blvd. Suite 240, Ogden, UT 84401

| | | | | |
|---------------------------------------|--|--|---|--|
| Date Submitted June 1, 2017 | Fees (Office Use) <u> </u> | Receipt Number (Office Use) <u> </u> | Priority Site (Office Use) <input type="radio"/> Yes <input checked="" type="radio"/> No | Permit Number (Office Use) 2017-50 |
|---------------------------------------|--|--|---|--|

| Property Owner/Authorized Representative Contact Information | | Project Information | |
|---|-------------------|--|-------------------|
| Name of Property Owner(s)/Authorized Representative(s) Daniel Dailey | | Project Name Dailey Residence | |
| Phone 801 633 7254 | Fax N/A | Project Address 13485 E. Hwy 39 Huntsville, Utah 84317 | |
| Email Address dancingmoosefarm@aol.com | | Estimated Project Length (mo) 18 month | |
| Mailing Address of Property Owner(s)/Authorized Representative(s) 1546 East Sunnyside Ave SLC, Utah 84005 | | Previous Permit No. (if applicable) | |
| | | Estimated Start Date July 15, 2017 | Actual Start Date |

Submittal Checklist

The application shall include a Storm Water Pollution Prevention Plan which meets the criteria set forth in Section 33-3-4 of the county ordinances.

The applicant shall file the application on or before the following dates:

- Subdivision:** The date that the applicant submits the preliminary subdivision development plat application.
- Site Plan:** The date that the applicant submits a site plan application or amended site plan.
- Building Permit:** The date that the applicant submits a building permit application if the applicant proposes to construct a building on an existing lot or parcel.
- Land Use Permit:** The date that the applicant submits a land use permit application.
- Other:** At least two (2) weeks before the developer intends to perform any type of work not listed above that would require a Storm Water Construction Activity Permit pursuant to this Chapter.

Failure to acquire a required Storm Water Construction Activity Permit is grounds for tabling a related subdivision application, site plan application, conditional use permit application, or building permit application. It is unlawful to commence work (move dirt) on a development site before obtaining a required Storm Water Construction Activity Permit.

Note: A pre-construction meeting is required before performing any on-site earth work, unless waived by the county engineer.

Applicant Narrative

Please explain your request.

storm water plan was submitted with weber county Building Permit application. Attached is a copy. our objective is to disturb very little area and follow the plan using silt fencing, maintain a clean work site have designated Dumpster area & cement truck clean out area and restroom facility.

Authorization

By signing below the Owner / Representative authorizes the county to enter the property to perform inspections.

| | |
|--|-----------------------------|
| Owner or Authorized Representative Signature Daniel Dailey | Date June 1, 2017 |
| Signature of Approval Paula [Signature] | Date 6-2-17 |

Storm Water Pollution Plan for:

Dailey Residence
13485 East Hwy 39
Huntsville, Utah 84317

Storm Water Manager and SWPPP Contacts:

Harvey Dalton
Dalton Construction
(801) 391-7887

Daniel Dailey
Owner
(801) 633-7254

Nature of Activity: Residence

The site slopes gradually from the Northeast to the Southwest. Site is well vegetated and we plan to preserve vegetation as much as possible.

The construction site to be disturbed will be less than 2,500 square feet. The total property is 17.85 acres. The area disturbed will be a small percentage of the total acreage.

Potential source of pollution: Construction Debris and truck cleaning (cement)


1. Our plan is to use silt fencing on the south and east side of build build site. Silt fencing will be installed prior to any work to commence. Silt fencing will be checked weekly.
2. Near the exit of job site we plan to have a designated trailer/dumpster for construction debris. All material will be covered to avoid litter and will be emptied prior to getting 75% full.
3. A designated concrete clean out area has been designated and all material will be removed from site upon completion of the project.
4. Area will be kept cleaned and debris will be disposed of properly.
5. All vehicles will be fueled off-site to eliminate the potential for pollutants from contaminating site.
6. Restroom (porta potty) will be provided on site close to build. Facility will be kept serviced by A-1.
7. Upon completion of the project the site will be landscaped with trees and seed will be planted in disturbed areas to re-vegetate area.

Attached is a map showing locations of the following designated areas:

1. Construction Site Exit
2. Dumpster Location
3. Cement Truck Clean-out
4. Restroom
5. Silt Fencing

Storm water Pollution Plan for:
Dailey Residence

(SWPPP)

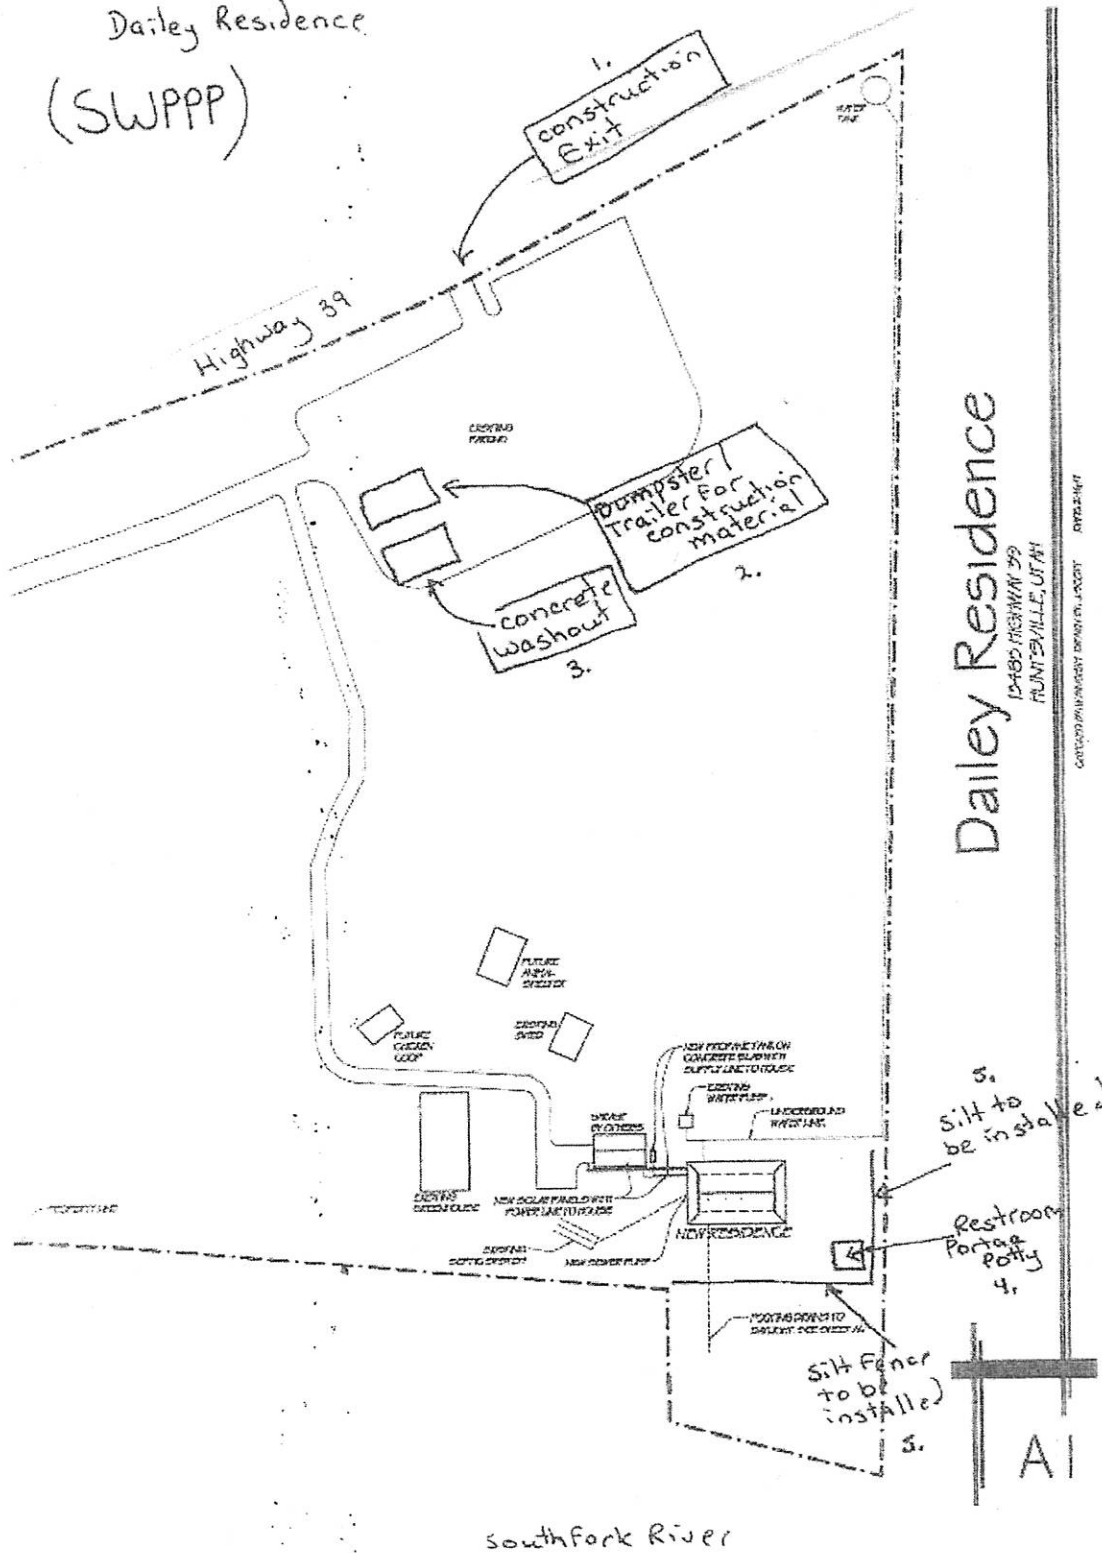

Dailey Residence

19485 HIGHWAY 39
MOUNTAIN VIEW, UTAH

CONSTRUCTION POLLUTION PREVENTION PLAN

Southfork River
