

OFFICE USE ONLY

Date Issued 9/3/10 By MMG Initial Inspection _____ By _____
 Water Table >34" Percolation Rate 15 MPI Final Inspection 10/01/10 By MG
 Septic Tank Size 1000gal Pumping Chamber Size 174 Total Absorption Area 570 Sq. Ft.

Type of System
☒ Conventional (includes absorption fields, and absorption beds)
☐ Seepage Trench
☐ At-Grade
☐ Mound
☐ Packed-Bed Media
☐ Renewal
☐ Alteration
☐ Holding Tanks*
☒ On-Site Training Center* State Fee added
☒ Plan Review Fee 1hr
☐ Tank Only
☐ Renewable Operating Permit - 2 yrs

Fee
\$231.00
 \$264.00
 \$528.00
 \$693.00
 \$693.00
 \$ 75.00
 \$ 0.00
 \$528.00
\$ 25.00
\$ 66.00 / hr
 \$132.00
 \$132.00


Pipe & gravel
399 1/2 cu yd

H.B. 14, passed by the legislature in the 2001 session, created a \$25.00 fee for all new underground wastewater treatment systems, beginning July 1, 2001. These fees will go into a new State restricted account to be used for the training, testing, and certification programs at the onsite training center.

Instructions

- ☒ Sized for maximum water usage of _____ GPD.
- ☒ Maximum depth to bottom of trench from original ground surface is 12"
- ☒ Call before rock is added to trench.
- ☒ Three foot maximum backfill over septic tank.
- ☒ Maintain 100 foot separation from ditches.
- ☒ Maintain 100 foot separation from wellhead.
- ☐ Install in designated location.
- ☐ Installation to begin only after approval of site conditions.
- ☒ On-site instruction prior to installation.
- ☒ Install according to construction plans reviewed by this office
- ☐ Two inspections required for ALL At-Grade Systems, installation and final cover.
- ☒ Operation & Maintenance required.
- ☒ Washed 3/4 to 2 1/2 inch gravel must be used. 1 inch minus will not be accepted.
- ☒ Water tightness test required. Tank must be full at time of inspection.
- ☒ Notify WMHD of installer's name prior to beginning installation.
- ☒ Locate system 50' from any slope greater than 35%

W:\wpwdoc\septic\oldfile\applica, ww permit.wpd

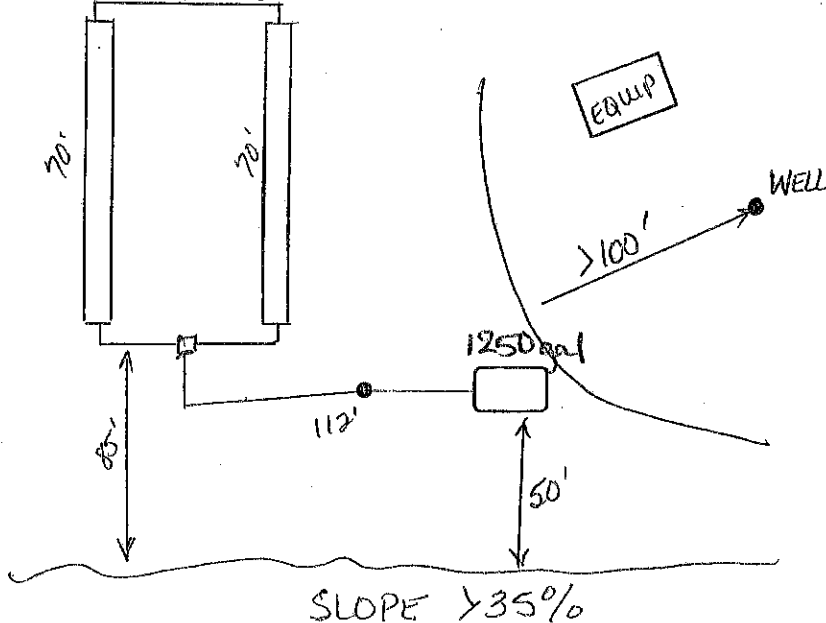

430 total sq. ft. installed
