



1" = 100'

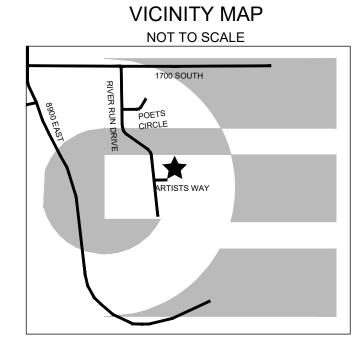

LEGEND

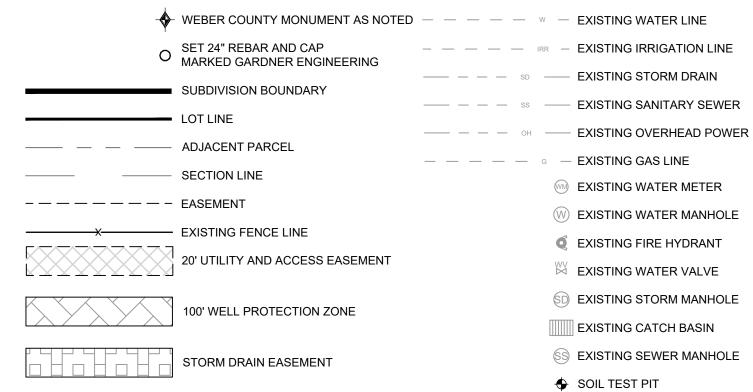

PERC TEST HOLE #	DEPTH INCHES	FINAL STABILIZED PERC RATE	TEST STATUS	RECOMMENDED WASTEWATER DISPOSAL SYSTEM	STATIFIED SOILS EVALUATION #1864 BY WEBER-MORGAN HEALTH DEPT
PT 21-L PT 21-M PT 21-H	60" 48" 36"	2.5 MIN/IN 5.0 MIN/IN 4.2 MIN/IN	FAIL PASS FAIL	AT-GRADE	0"-16" LOAM, GRAY, DRY, GRAVELLY &COBBLY 16"-64" SANDYLOAM, REDDISH BROWN, DRY, VERY GRAVELLY, COBBLY & STONEY
PT 22-L PT 22-M PT 22-H	60" 48" 36"	5.6 MIN/IN 6.2 MIN/IN 5.0 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-17" LOAM, GRAY, DRY, GRAVELLY, COBBLY & STONEY 17"-65" SANDY SKELETAL, DARK REDDISH BROWN, DRY
PT 23-L PT 23-M PT 23-H	60" 48" 36"	5.0 MIN/IN 5.6 MIN/IN 25.0 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-14" LOAM. GRAY, DRY, GRAVELLY & COBBLY 14"-32" SANDY LOAM, LIGHT GRAY, VERY GRAVELLY & COBBLY 32"-65" SANDY SKELETAL, PALE BROWN, DRY
PT 24-L PT 24-M PT 24-H	60" 48" 36"	4.5 MIN/IN 2.9 MIN/IN 25.0 MIN/IN	FAIL FAIL PASS	WISCONSIN MOUND	0"-18" LOAM, GRAY, MOIST, GRAVELLY 18"-36" LOAM, GRAYISH BROWN, MOIST, GRAVELLY 36"-45" HEAVY LOAM, BROWN, MOIST, GRAVELLY & STONEY 45"-60" SANDY LOAM, BROWN, MOIST, VERY COBB;Y & STONEY
PT 25-L PT 25-M PT 25-H	60' 48" 36"	8.3 MIN/IN 2.5 MIN/IN 7.1 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-26" LOAM, BLACK, MOIST GRAVELLY, COBBLY 26"-42" SANDY LOAM, PALE BROWN, DRY, VERY COBBLY, STONEY 42"-60" LOAMY SAND, PALE BROWN, DRY, VERY COBBLY, STONEY
PT 26-L PT 26-M PT 26-H	60" 48" 36"	5.0 MIN/IN 12.5 MIN/IN 4.5 MIN/IN	PASS PASS FAIL	CONVENTIONAL	0"-6" LOAM, GRAY, DRY, GRAVELLY, COBBLY, STONEY 6"-38" SANDY LOAM, PALE BROWN, DRY, VERY COBBLY, STONEY LOAMY SAND, REDDISH BROWN, MOIST, VERY COBBLY, STO
PT 27-L PT 27-M PT 27-H	60" 48" 36"	8.3 MIN/IN 7.1 MIN/IN 5.6 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-8" LOAM, GRAY, DRY, COBBLY & STONEY 8"-36" SANDY LOAM, GRAY, DRY, VERY COBBLY & STONEY 36"-57" SANDY SKELETAL, REDDISH BROWN, MOIST, COBBLY & STO
PT 28-L PT 28-M PT 28-H	60" 48" 36"	4.2 MIN/IN 5.0 MIN/IN 5.6 MIN/IN	FAIL PASS PASS	AT-GRADE	0"-10" LOAM, GRAY, DRY, COBBLY & STONEY 10"-27" SANDY LOAM, PALE BROWN, DRY, VERY COBBLY & STON 27"-55" SANDY SKELETAL, REDDISH BROWN, MOIST
PT 29-L PT 29-M PT 29-H	60" 48" 36"	8.3 MIN/IN 5.0 MIN/IN 8.3 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-14" LOAM. GRAY, DRY, GRAVELLY 14"-28" LOAM, GRAYISH BROWN, GRAVELLY, DRY 28"-58" SANDY LOAM, REDDISH BROWN, DRY, COBBLY & STONEY
PT 30-L PT 30-M PT 30-H	60" 48" 36"	8.3 MIN/IN 5.0 MIN/IN 10.0 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-17" LOAM, GRAY, DRY, VERY GRAVELLY 17"-48" LOAMY SKELETAL, DARK REDDISH BROWN, DRY
PT 31A-L PT 31A-M PT 31A-H	60" 48" 36"	1.2 MIN/IN 5.0 MIN/IN 16.7 MIN/IN	FAIL PASS PASS		0"-16" LOAM, BLACK, MOIST, GRAVELLY 16"-36" LOAM, BROWN, MOIST, GRAVELLY & STONEY 36"-60" SANDY SKELETAL, REDDISH BROWN, MOIST
PT 31B-L PT 31B-M PT 31B-H	60" 48" 36"	8.3 MIN/IN 6.2 MIN/IN 5.5 MIN/IN	PASS PASS PASS	CONVENTIONAL	0"-27" SILT LOAM, BLACK, MOIST, GRAVELLY 27"-41" LOAM, GRAYISH BROWN, MOIST, GRAVELLY 41"-52" LOAM, BROWN, MOIST 52"-68" SANDY LOAM, BROWN, MOIST

SOIL LOG #14902 LOCATION - UTM ZONE 12 NAD 83 439440E 4564344N. CULINARY WATER WELL MUST BE A MINIMUM OF 100 FEET FROM WASTE WATER FACILITIES.

